

# memorandum

Idaho Operations Office  
West Valley Project Office


DATE: May 17, 1991

SUBJECT: Waste Tank Farm Processing Schedule Update

TO: Ted McIntosh, EM 343  
Project Manager for West Valley  
U. S. Department of Energy

Attached for your information is a weekly update of the Level II Schedule for Resumption of Waste Tank Farm Processing. Dates which have changed by more than ten working days from the previous schedule are highlighted with a "number". This number corresponds to a brief explanation of the reason for the schedule change. This explanation is contained in an attachment to the schedule.

If you have questions or comments, please call me at FTS 473-4780.



J. Alan Yeazel, Manager  
Operations, Maintenance,  
Engineering and Construction  
West Valley Project Office

## Attachment

cc: R. Davis Hurt, NRC-HQ, (w/att)  
J. Roth, NRC, Region 7, (w/att)  
D. B. Engelman, DOE-ID, (w/att)  
S. G. Harbison, NYSERDA, (w/att)

AY:033:91 - 0635:91:03

AY/sl



# OPEN PLAN (tm)

Report: NOFLOWAY  
Project: HLWSTART  
Time Now: 15MAY91  
Date: 15MAY91  
Page: 13 35 58

## WASTE TANK FARM PROCESSING



ACT NUM ES DATE EDATE OUR STATUS

### AUSTIC ADDITION SYSTEM

CHAD0001 15MAY91 29AUG91 107 Future  
CHAD0020 19APR91 07JUN91 30 Started  
CHAD0050 10JUN91 05AUG91 40 Future  
CHAD0060 30AUG91 29AUG91 0 Future

### CRITICALITY MONITOR DESIGN

CRIC0001 15MAY91 20SEP91 129 Future  
CRIC0020 15MAY91 19APR91 15 COMPLETE  
CRIC0040 21MAY91 24JUN91 45 Future  
CRIC00130 02AUG91 15AUG91 10 Future  
CRIC00150 09SEP91 20SEP91 10 Future

### EVAPORATOR RECOVERY


EVPR0001 15MAY91 01JUN91 48 Future  
EVPR00270 18FEB91 01MAR91 10 COMPLETE  
EVPR00280 11MAR91 22MAR91 10 COMPLETE  
EVPR00282 27MAR91 05MAY91 20 COMPLETE  
EVPR00255 04JUN91 10JUN91 5 Future

### EA 17 / WASTE QUAL. CATION

HEWD0001 15MAY91 08OCT91 147 CRITICAL  
HEWD0005 22APR91 02MAY91 3 COMPLETE  
HEWD0032 01MAY91 02MAY91 2 COMPLETE  
HEWD0410 06MAY91 17MAY91 5 CRITICAL  
HEWD0212 25JUN91 25JUN91 1 Future  
HEWD1000 22JUL91 02AUG91 10 Future  
HEWD0145 01AUG91 07AUG91 5 Future  
HEWD4400 01AUG91 24OCT91 60 Future

### Legend

■ = In progress  
□ = Planned  
□ = Critical

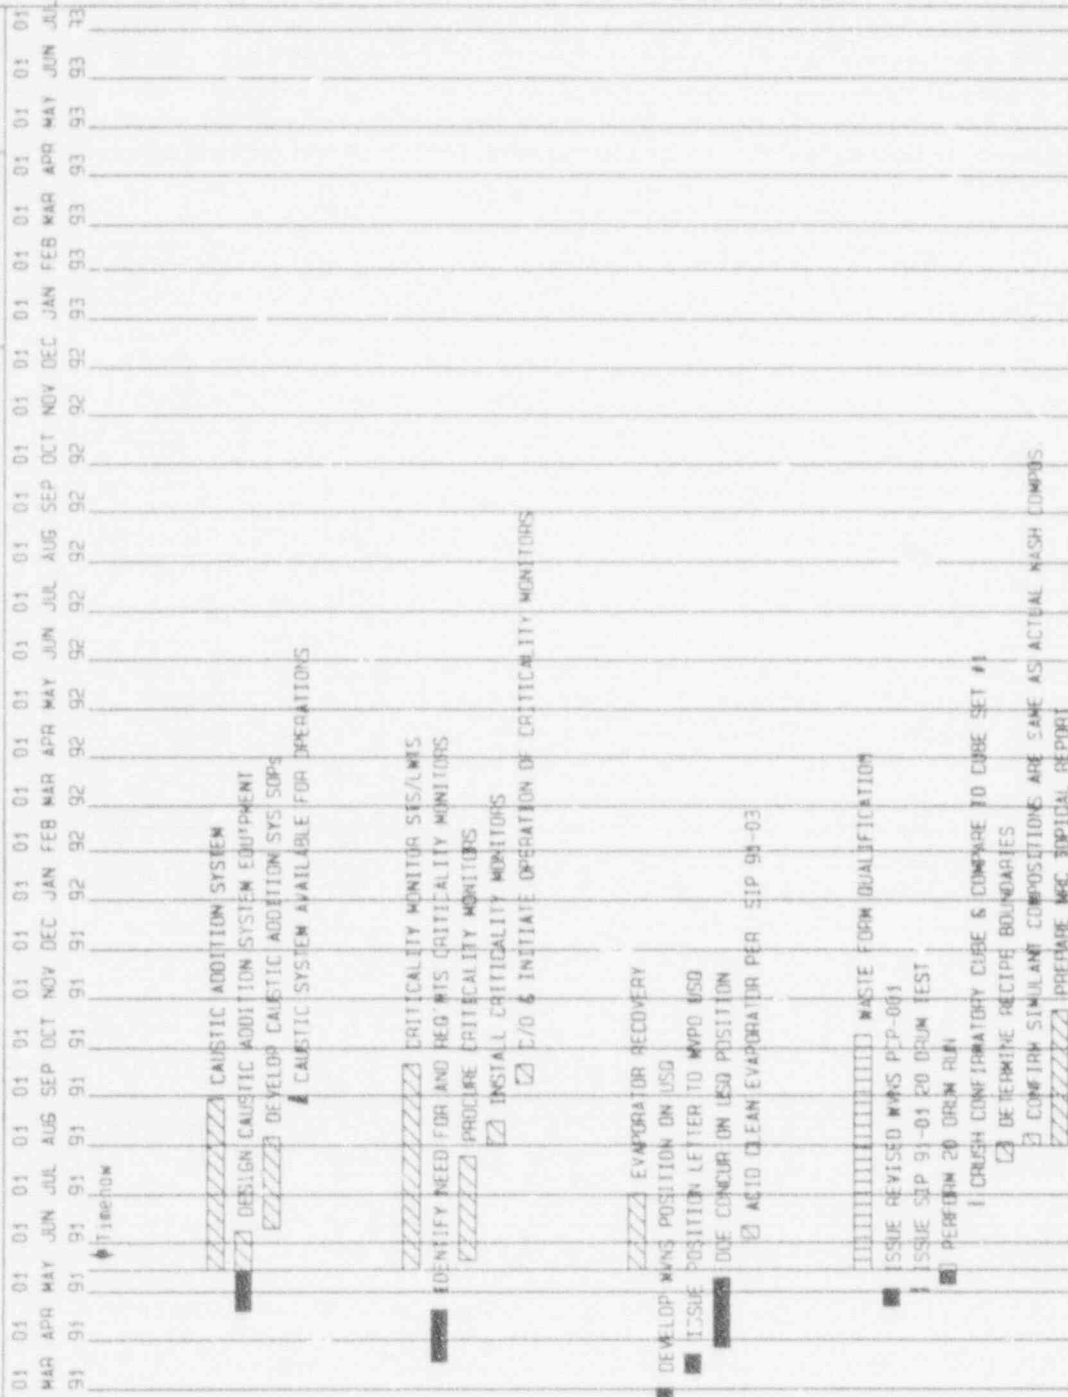

### Signatures

Prep S. K. Andrus

Appr P. S. Klenian

All characters represent 7 time unit(s)



# WASTE TANK FARM PROCESSING



West Valley  
Nuclear  
Services

OPEN PLAN (tm)

Report: NOFLOAY  
Project: HLWSTART  
Time Now: 15MAY91  
Date: 15MAY91  
Time: 13 35 58  
Page: 2

ACT NUM EDATE EDATE OUR STATUS

QRB

JRR00001 15MAY91 30SEP91 139 Future  
JRR00002 17APR91 17MAY91 10 Started  
JRR00040 04JUN91 30JUN91 40 Future  
JRR000200 15AUG91 19AUG91 3 Future  
JRR000210 20AUG91 03SEP91 10 Future  
JRR000300 17SEP91 30SEP91 10 Future

-01 & B-02 PUMP FIX AND INSTALLATION


PMP00001 15MAY91 05SEP91 79 Future  
PMP000700 27MAR91 27MAR91 20 COMPLETE  
PMP00180 01APR91 04APR91 4 COMPLETE  
PMP00290 05APR91 15MAY91 15 Started  
PMP00204 12APR91 15APR91 4 COMPLETE  
PMP00195 05JUN91 08JUN91 4 Future  
PMP00256 20JUN91 03JUL91 10 Future  
PMP00210 25JUN91 09JUL91 10 Future  
PMP00405 10JUL91 11JUL91 2 Future  
PMP00412 12JUL91 15JUL91 2 Future  
PMP00422 16JUL91 17JUL91 2 Future  
PMP00442 18JUL91 19JUL91 2 Future  
PMP00432 05AUG91 06AUG91 2 Future  
PMP00452 16AUG91 20AUG91 3 Future  
PMP00460 20AUG91 19AUG91 0 Future  
PMP00720 05SEP91 05SEP91 1 Future

NTS SAR LEADERS AND APPROVALS

STS00001 15MAY91 01OCT91 140 Future  
LMT00142 07AUG91 09AUG91 3 Future  
LMT00144 12AUG91 23SEP91 30 Future

Legend

■ = In progress  
□ = Planned  
▨ = Critical

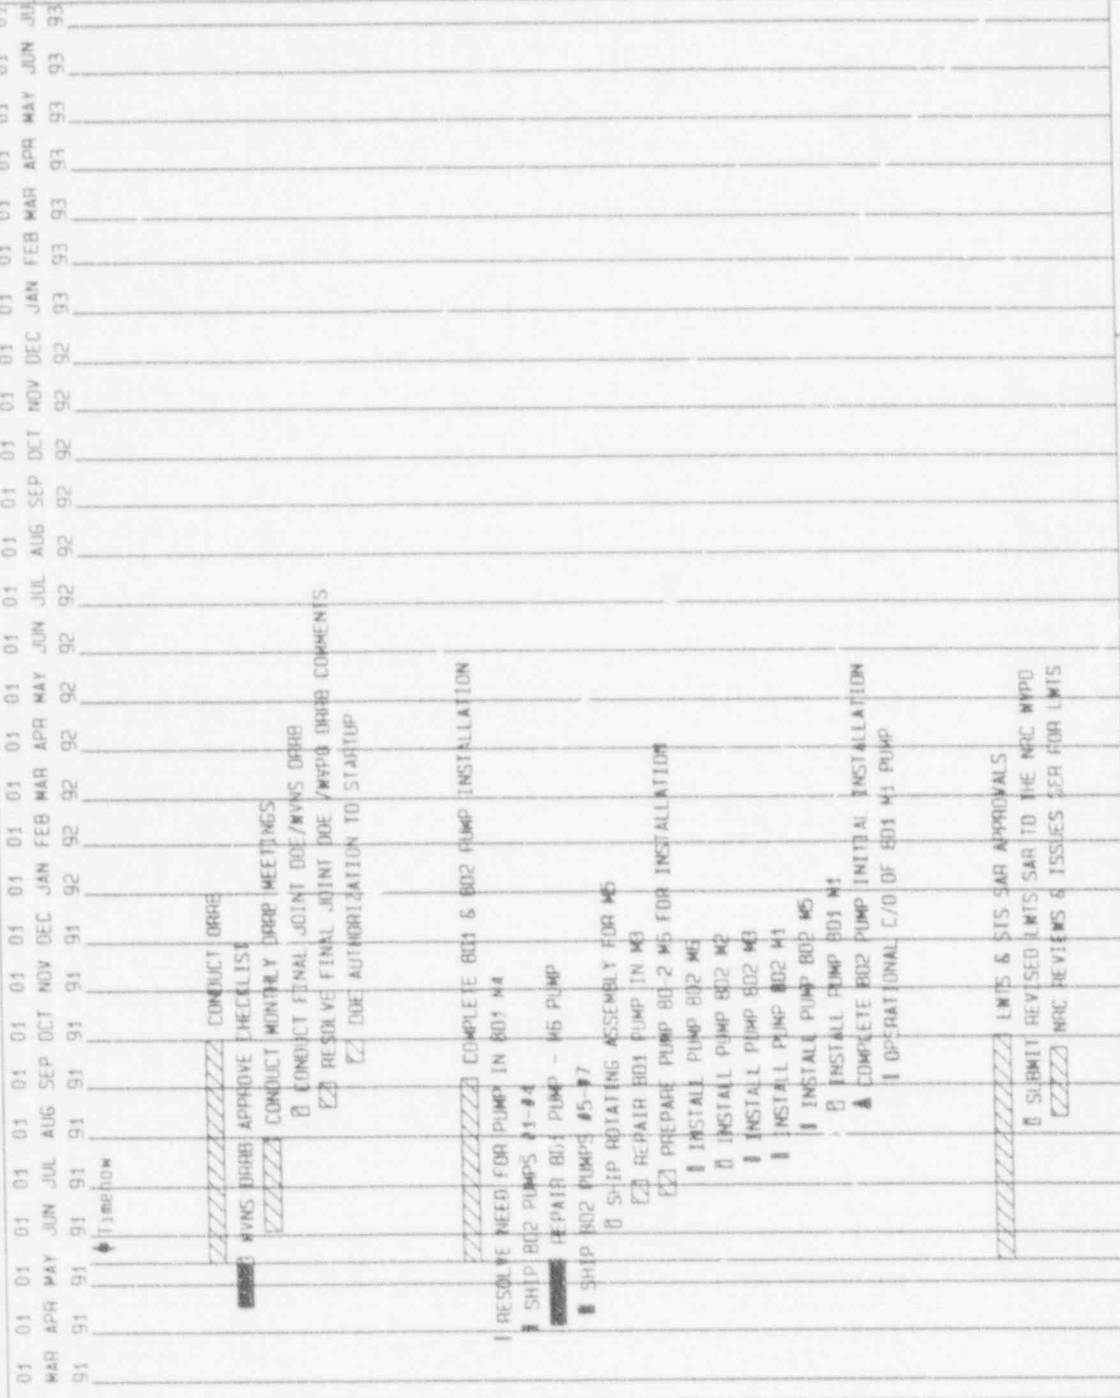

Signatures

Prep S. K. Andrus  
Appv P. S. Kianian

All characters represent 7 time unit(s)




# OPEN PLAN (tm)

Report: NOFLOAY  
Project: HLWSTART  
Time Now: 15MAY91  
Date: 15MAY91  
Time: 13:35:58  
Page: 3

CT NUM ESDATE EFOATE DUR STATUS

## WASTE TANK FARM PROCESSING



West Valley  
Nuclear  
Services

### SAR UPDATES AND APPROVALS

TS000015	27MAY91	27APR91	15	COMPLETE
TS000030	03MAY91	10MAY91	10	COMPLETE
TS000040	03JUN91	07JUN91	5	Future
TS000045	03JUN91	07JUN91	5	Future
TS000060	01JUL91	15JUL91	10	Future
TS000140	18JUL91	22JUL91	3	Future
TS000160	04SEP91	01OCT91	20	Future

### ITS STARTUP

IRP000001	05OCT91	17NOV92	406	Future
IRP000110	05OCT91	15OCT91	5	Future
IRP000220	13NOV91	03DEC91	21	Future
IRP000250	04DEC91	10DEC91	5	Future
IRP000100	20DEC91	30DEC91	5	Future
IRP000270	15JAN92	28JAN92	10	Future
IRP000300	23JAN92	04FEB92	5	Future
IRP000400	26FEB92	10MAR92	10	Future
IRP000500	13MAR92	10MAR92	0	Future
IRP000605	11MAR92	17NOV92	252	Future

### TITANIUM ZEOLITE

ITZ000001	15MAY91	08JAN92	239	Future
ITZ000150	26APR91	10MAY91	1	COMPLETE
ITZ000115	15MAY91	04OCT91	100	Future
ITZ000180	30MAY91	31MAY91	2	Future
ITZ000210	06JUN91	12JUN91	7	Future
ITZ000220	17JUN91	17JUN91	1	Future
ITZ000240	09AUG91	15AUG91	6	Future
ITZ000270	19AUG91	09SEP91	15	Future
ITZ000265	10SEP91	11SEP91	2	Future
ITZ000312	23OCT91	08JAN92	10	Future

### Legend

■ = In progress  
 [ ] = Planned  
 [ ] = Critical



Signatures

Prep S. K. Andrus  
 Appr P. S. Klianian

All characters represent 7 time unit(s)



## CEMENT SOLIDIFICATION DOCUMENTATION



OPEN PLAN (tm)

```
Report: NOFLOSK
Project: HLWSTART
Time Now: 15MAY91
Date: 16MAY91
Time: 13 39.34
Page: 1
```

Page	EC DATE	EFF DATE	OUR STATUS
1			
2			
3			
4			
5			
6			
7			
8			
9			
10			
11			
12			
13			
14			
15			
16			
17			
18			
19			
20			
21			
22			
23			
24			
25			
26			
27			
28			
29			
30			
31			
32			
33			
34			
35			
36			
37			
38			
39			
40			
41			
42			
43			
44			
45			
46			
47			
48			
49			
50			
51			
52			
53			
54			
55			
56			
57			
58			
59			
60			
61			
62			
63			
64			
65			
66			
67			
68			
69			
70			
71			
72			
73			
74			
75			
76			
77			
78			
79			
80			
81			
82			
83			
84			
85			
86			
87			
88			
89			
90			
91			
92			
93			
94			
95			
96			
97			
98			
99			
100			

MENT / WASTE QUALIFICATION

HE N00035	12MAR91	25MAR91	10	COMPLETE
HE N00042	27MAR91	02APR91	5	COMPLETE
HE N00043	27MAR91	18APR91	10	COMPLETE
HE N00082	27MAR91	30APR91	5	COMPLETE
HE N00216	27MAR91	30APR91	10	COMPLETE
HE N04119	27MAR91	30APR91	10	COMPLETE
HE N04118	27MAR91	03MAY91	10	COMPLETE
HE N00092	29MAR91	05APR91	10	COMPLETE
HE N04005	03APR91	22APR91	10	COMPLETE
HE N00041	03APR91	22APR91	5	COMPLETE
HE N00094	03APR91	29APR91	10	COMPLETE
HE N00214	15APR91	02MAY91	10	COMPLETE
HE N00084	17APR91	21MAY91	5	Started
HE N004190	20MAY91	17JUN91	20	Future
HE N00088	05JUN91	03JUL91	20	Future
HE N01001	05AUG91	30AUG91	20	Future
HE N00146	08AUG91	05SEP91	20	Future
HE N00215	09OC191	05NOV91	20	Future
HE N04121	09OC191	05NOV91	20	Future
HE N04410	25OC191	25OC191	1	Future
HE N04420	28OC191	25OC191	40	Future
HE N04006	22APR91	02MAY91	3	COMPLETE
HE N00032	01MAY91	02MAY91	2	COMPLETE
HE N00100	22JUL91	02AUG91	5	Future
HE N00145	01AUG91	07AUG91	10	Future
HE N04400	01AUG91	26OC191	60	Future

WAYS STARTING

Account	Period	Future
SUP00270	15JAN92	10
SUP00300	29JAN92	5

Legend

- = In progress
- ▨ = Planned
- ▩ = Critical

all characters represent 7 time unit(s)

Signatures

S. K. Andrus

Anur. P. S. Klianin
