


040066592905

40-6659

July 9, 1985

RETURN ORIGINAL TO PDR, HQ.

Dr. Harry J. Pettengill, Chief
 Licensing Branch 2
 U.S. Nuclear Regulatory Commission
 Uranium Recovery Field Office, R IV
 P.O. Box 25325
 Denver, Colorado 80225

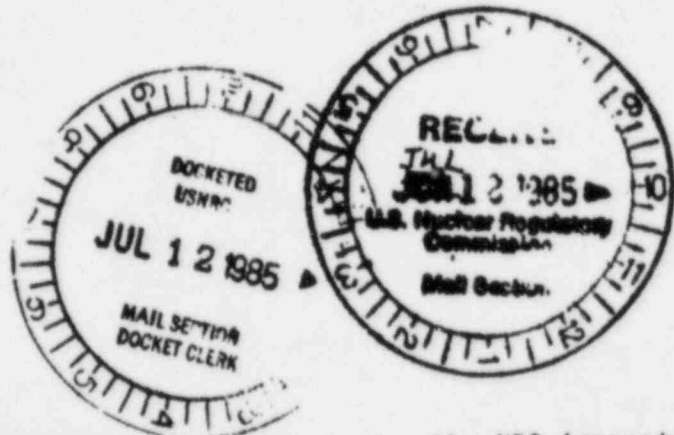

Gentlemen:

The following information is provided as suggested during the NRC inspection of June 17th and 20th. The Petrotomics Mill complex will be decommissioned using a phased approach. The Phase Plan was provided to Mr. Konwinski and Mr. Shoppen during the inspection. The progress on this plan as of July 8 is as follows.

Phase I

Primary Crusher - - completed except for demolition of concrete.
 Secondary Crusher - - Completed.
 Fine Ore Storage Bins - - Roof and siding removed.
 Carpenter Shop - - Roof and siding removed.
 'B' Pump House - - Roof and siding removed, pumps removed.
 'C' Pump House - - Approximately 50% completed.
 # 1 thru # 6 80' Thickeners - - Approximately 90% completed.
 Clariflocculator Tank - - Completed.
 Diesel Storage Tank - - Completed.
 Two Salt Storage Tanks - - Completed.
 Acid Pump Pad - - 50% Completed.
 55' Thickeners - - 80% Completed.

Phase II

Tails Building - - 35% Completed.
 Acid Tank (A) - - 80% Completed-work being done by Pathfinder.

8508190317 850709
 PDR ADOCK 04006659
 C PDR

FEE EXEMPT

Add Info
 00718

Phase III

Electric Shop - - Completed-work done by Pathfinder.


Portable Offices - - Completed-work done by Pathfinder.

Phase IV

Main Mill Building - - Some roofing has been removed to gain access to equipment on which we are negotiating the sale.

We will continue to file these reports to keep you informed of the progress of the decommissioning of the mill. Should you have any questions please feel free to contact me at (307) 356-4341.

Sincerely,



Stephen J. Pfaff
Radiation Coordinator

SJP/mp

Attachment: Phase Plan

PHASE I

PRIMARY CRUSHER

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Disconnect Electrical	Electrician	----
Siding	Contractor	----
Bury Siding	Crew I	Bury
Coarse Ore Grizzly	Crew I	Salvage/Bury
Electrical	Electrician	" "
Apron Feeder	Crew I	" "
Vibrating Grizzly	Crew I	" "
Jaw Crusher	Crew I	" "
Chutes	Crew I	Bury
Scavenger Belt	Crew I	"
Dust Collector	Crew I	"
#1 & #2 Belts	Crew I	"
#1 & #2 Conveyors	Contractor	Lay Down Area
Transformer Tower	Contractor	Bury
Structures	Contractor	Salvage/Bury
Concrete	Contractor	Break up in Place

SECONDARY CRUSHER

Disconnect Electrical	Electrician	----
Siding	Contractor	----
Bury Siding	Crew II	Bury
Electrical	Electrician	Salvage/Bury
Magnet	Crew II	" "
Chute to Screen	Crew II	Bury
Screen System	Crew II	Salvage/Disposal
Chute to Impactor	Crew II	Bury
Dust Collector	Crew II	"
Impactor	Crew II	Salvage/Bury

SECONDARY CRUSHER (Con't)

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
#3 Belt	Crew II	Bury
#3 Conveyor	Contractor	Lay Down Area
Structures	Contractor	Salvage/Bury
Concrete	Contractor	Break up in Place

FINE ORE STORAGE BINS

Disconnect Electrical	Electrician	----
Roof	Contractor	----
Bury Roof	Crew III	Bury
Siding	Contractor	----
Bury Siding	Crew III	Bury
Electrical	Electrician	----
Tripper	Crew III	Bury
#1 & #2 Feeder Belts	Crew III	"
#1 & #2 Feeders	Crew III	Salvage/Bury
#4 Belt	Crew III	Bury
Weightometer	Crew III	Salvage
#4 Conveyor	Contractor	Lay Down Area
Clarifloculator Sump Pump	Crew III	Salvage/Bury
#1 & #2 Bins	Contractor	" "
Structures	Contractor	" "
Concrete	Contractor	Break up in Place

CARPENTER SHOP

Disconnect Electrical	Electrician	----
Electrical	Electrician	----
Roof	Contractor	----
Bury Roof	Crew IV	Bury
Siding	Contractor	----
Bury Siding	Crew IV	Bury
Fuel Oil Feed Pumps	Crew IV	Salvage/Bury
Fuel Oil Lines	Crew IV	Bury

'B' PUMPHOUSE

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Disconnect Electrical	Electrician	----
Roof	Contractor	----
Bury Roof	Crew I	Bury
Siding	Contractor	----
Bury Siding	Crew I	Bury
#1-#2-#3 U'Flow Pumps	Crew I	Salvage/Bury
#1-#2-#3 U'Flow Troughs	Crew I	Bury
Electrical	Electrician	----
#1-#2-#3 Launderers	Crew I	Bury
Underflow Piping	Crew I	"
Overflow Pumps	Crew I	Salvage/Bury
Standby Pump	Crew I	" "
Sump Pump	Crew I	" "
Transfer Pumps	Crew I	" "
Surge Vessels	Crew I	" "
Piping	Crew I	Bury
Structures	Contractor	Salvage/Bury

'C' PUMPHOUSE

Disconnect Electrical	Electrician	----
Roof	Contractor	----
Bury Roof	Crew I	Bury
Siding	Contractor	----
Bury Siding	Crew I	Bury
#1-#2-#3 U'Flow Pumps	Crew I	Salvage/Bury
#1-#2-#3 U'Flow Troughs	Crew I	Bury
Electrical	Electrician	----
#1-#2-#3 Launderers	Crew I	Bury
Underflow Piping	Crew I	Bury
Overflow Pumps	Crew I	Salvage/Bury
Standby Pumps	Crew I	" "
Sump Pump	Crew I	" "
Transfer Pumps	Crew I	" "
Surge Vessels	Crew I	" "
Piping	Crew I	Bury
Structures	Contractor	Salvage/Bury

#1 THRU #6 - 80' THICKENERS

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Electrical	Electrician	----
Feed Launder	Crew II	Bury
Feed Box	Crew II	Bury
Piping	Crew II	Bury
Rake	Contractor	Salvage/Bury
Rake Mechanism	Contractor	" "
Structure	Contractor	" "
Thickener	Contractor	Bury
Clean Beds Off Floors	Crew II	Bury
Floor (Wooden)	Contractor	Bury
Concrete	Contractor	Break up in Place
Walkway From 55's	Contractor	Salvage Bury
Walkway to 'C' P.H.	Contractor	" "

55' THICKENERS

Maintenance

CLARIFLOCCULATOR TANK

Disconnect Electrical	Electrician	----
Electrical	Electrician	----
Rake	Contractor	Bury
Rake Mechanism	Contractor	Salvage/Bury
Walkway Structure	Contractor	" "
Tank	Contractor	Bury
Tank Floor	Contractor	"

DIESEL STORAGE TANK

Disconnect Piping	Crew III	Bury
Move Tank	Crew III	Lay Down Area

KERMAC STORAGE TANKS

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Move Above Ground Tanks (2)	Crew III	Lay Down Area
Uncover Underground Tank	Crew III	----
Move Underground Tank	Crew III	Lay Down Area

TWO SALT STORAGE TANKS

Maintenance

THREE GASOLINE STORAGE TANKS

Disconnect Electrical	Electrician	----
Dig Up Tank By Lab	Crew III	Bury
2 Tanks Behind Amb. Garage	Crew III	Lay Down Area
Remove Pumps	Crew III	Lay Down Area
Remove Guard Rail	Crew III	Bury

NH₃ TANK

Insure Tank Empty	Crew IV	----
Disconnect Piping	Crew IV	Bury
Remove Pump	Crew IV	Salvage/Bury
Remove Tank	Contractor	Lay Down Area
Concrete	Contractor	Break up in Place
Guard Rail	Crew IV	Bury

TWO MILL PROPANE TANKS

Insure Tank Empty	Crew IV	----
Disconnect Piping	Crew IV	Bury
Remove Pumps	Crew IV	Salvage/Bury
Guard Rail	Crew IV	Bury
Tanks	Contractor	Lay Down Area
Concrete	Contractor	Break up in Place

TWO LAB PROPANE TANKS

Insure Tanks Empty	Crew IV	----
Disconnect Piping	Crew IV	Bury
Remove Guard Rail	Crew IV	Bury
Tanks	Crew IV	Lay Down Area

MITCHEL PROPANE VAPORIZERS

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Disconnect Piping	Crew I	Bury
Shed	Crew I	Bury
Guard Rail	Crew I	Bury
Vaporizers	Crew I	Salvage/Bury

WATER BATH PROPANE VAPORIZERS

Disconnect Electrical	Electrician	----
Disconnect Piping	Crew I	Bury
Vaporizers	Crew I	Lay Down Area

TRANSFORMER YARD

Electrical	Electrician	----
Fencing	Crew II	Bury
Poles	Electrician/Contractor	Bury
Transformers	Contractor	Lay Down Area

ACID PUMP PAD

Electrical	Electrician	----
Pumps	Crew II	Salvage/Bury
Piping	Crew II	Bury
Concrete	Crew II	Break up in Place

EMERGENCY ELECTRICAL GENERATORS

Electrical	Electrician	----
Fuel Piping	Crew III	Bury
Remove South Siding	Crew III	Salvage/Bury
Remove Generators	Contractor	Lay Down Area

STEAM BOILERS & RELATED EQUIPMENT

Electrical	Electrician	----
Disconnect Piping	Contractors	Bury
Remove Boilers	Contractors	Lay Down Area
Related Equipment	Crew IV	Lay Down Area

WATER SOFTENERS & FILTERS

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Electrical	Electrician	----
Disconnect Piping	Contractors	Bury
Filters	Crew IV	Lay Down Area
Softeners	Crew IV	Lay Down Area
Condensate Pumps	Crew IV	Salvage/Bury
Condensate Tank	Contractors	Lay Down Area
Sump Pump	Crew IV	Lay Down Area
Grating	Crew IV	Bury
Salt Tank	Crew IV	Lay Down Area

LOWER QUONSET WAREHOUSE

Electrical	Electrician	----
Quonset	Contractors	Lay Down Area

(If Not Sold In Place)

RADIATION STORAGE BUILDING

Building	Crew I	Bury
----------	--------	------

TRAINING BUILDING

Electrical	Electrician	----
Remove/Store Contents	Crew I	----
Building	Crew I	Lay Down Area

(Or Use For Contractor)

CAFETERIA BUILDING

Electrical	Electrician	----
Remove Contents	Crew II	Salvage/Bury
Building	Contractor	Salvage/Bury
Concrete	Contractor	Break up in Place

(Building may be Sold)

(2) SOUTH & EAST MOTEL BUILDINGS

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Electrical	Electrician	----
Remove Contents	Crew II	Salvage/Bury
Building	Contractor	Salvage/Bury
Concrete	Contractor	Break up in Place
	(Building may be Sold)	

MILL ANALYTICAL LAB BUILDING

Electrical	Electrician	----
Remove Contents	Crew II	Salvage/Bury
Building	Contractor	Bury

RADIATION LAB BUILDING

Electrical	Electrician	----
Remove Contents	Crew III	Salvage/Bury
Building	Contractor	" "
Concrete	Contractor	Break up in Place

OIL STORAGE BUILDING

Electrical	Electrician	----
Building	Crew III	Bury
Concrete	Contractor	Break up in Place

PAINT STORAGE BUILDING

Electrical	Electrician	----
Piping	Crew III	Bury
Building	Crew III	Lay Down Area

(END OF PHASE ONE)

WCG/5.23.85/ow

PHASE II

SX-1, SX-2, SX-3 BUILDINGS

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Electrical	Electrician	----
	<u>'A'</u> <u>FOAM ROOM</u>	
Piping	Crew I	Bury
Foam Tank	Crew I	Bury
Valves	Crew I	Salvage/Bury
Pumps	Crew I	" "
	<u>'B'</u> <u>FOAM ROOM</u>	
MCC Panels	Electrician	Salvage/Bury
	<u>'C'</u> <u>SX LAB</u>	
Electrical	Electrician	Salvage/Bury
Piping	Crew II	" "
Consoles	Electrician	" "
Cabinets	Crew II	Bury
	<u>'D'</u> <u>SX-1</u>	
Roof	Contractor	Bury
Siding	Contractor	Bury
Walkways	Crew III	Bury
Pumps	Crew III	Salvage/Bury
Lewis Baffles	Crew III	Bury
Wooden Baffles	Crew III	"
Piping	Crew III	"
Pipe Rack	Contractor	Salvage/Bury
Weirs	Crew III	Bury
BP & PO Tanks	Contractor	Salvage/Bury
Steel Structures	Contractor	" "
Concrete	Crew III/Contractors	Break up in Place

<u>Item</u>	<u>'E'</u> <u>SX-2</u> <u>Responsibility</u>	<u>Disposal</u>
Roof	Contractor	Bury
Siding	Contractor	Bury
Decking	Crew IV	Bury
Pumps	Crew IV	Salvage/Bury
Wooden Baffles	Crew IV	Bury
Piping	Crew IV	Bury
Pipe Rack	Contractor	Salvage/Bury
Weirs	Crew IV	Bury
Steel Structure	Contractor	Salvage/Bury
BO & PO Tanks	Contractor	" "
Concrete	Crew IV/Contractor	Break up in Place

	<u>'F'</u> <u>SX-3</u>	
Roof	Contractor	Bury
Siding	Contractor	Bury
Walkways	Crew I	Bury
Pumps	Crew I	Salvage/Bury
Wooden Baffles	Crew I	Bury
Piping	Crew I	Bury
Pipe Rack	Contractor	Salvage/Bury
Weirs	Crew I	Bury
Steel Structures	Contractor	Salvage/Bury
BO & PO Tanks	Contractor	" "
Organic Mix Tank	Contractor	" "
Concrete	Crew I/Contractor	Break up in Place

	<u>'G'</u> <u>SX LAB - MCC - FOAM ROOM</u>	
Building	Contractor	Bury
Concrete	Contractor	Break up in Place

YELLOWCAKE BUILDING & TANKS

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Electrical	Electrician	----
Roof	Contractor	Bury
Siding	Contractor	Bury
Steel Structure	Contractor	Salvage/Bury
Piping	Crew II	Bury
Pumps	Crew II	Salvage/Bury
A & B Tank Agitators	Crew II	Lay Down Area
A & B Tanks	Crew II	Lay Down Area
Steel Walkways	Contractor	Bury
Wooden Tank Covers	Crew II	"
Concentrate Thickener	Contractor	Tails
Wash Thickener	Contractor	Tails
Sump Pump	Crew II	Bury

TAILS BUILDING

Electrical	Electrician	Salvage/Bury
Roof	Contractor	Bury
Siding	Contractor	Bury
Steel Structure	Contractor	Salvage/Bury
Pumps	Crew III	" "
Piping	Crew III	Bury
Decking & Stairs	Contractor	Salvage/Bury
Tailings Vessel	Contractor	" "
Concrete	Contractor	Break up in Place
Concrete Apron (North)	Contractor	" " "

RAFFINATE SURGE TANK

Tank	Crew IV	Bury
Concrete	Contractor	Break up in Place

RECLAIM SURGE TANK

Tank	Crew IV	Bury
Concrete	Contractor	Break up in Place

PREGNANT SOLUTION TANK

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Tank	Contractor	Bury
Concrete	Contractor	Break up in Place

CLARIFLOC SURGE TANK

Tank	Crew I	Bury
Concrete	Contractor	Break up in Place

ACID TANKS

(A)

Western Tank (Large)	Western Nuclear	Western Nuclear
Concrete	Contractor	Break up in Place

(B)

Horizontal Tank	Western Nuclear	Western Nuclear
Concrete	Contractor	Break up in Place

(C)

Small Vertical Tank	Crew I	Bury
---------------------	--------	------

NAC10₃ STORAGE TANKS (PITS)

Electrical	Electrician	----
Pump	Crew II	Salvage/Bury
Piping	Crew II	Bury
Covers	Crew II	"
Cover Over Basement	Crew II	"
Concrete	Crew II	Break up in Place

Note: Wet down area - Use Large Backhoe

(4)

DRYER SCRUBBER TANKS

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Electrical	Electrician	----
Pumps	Crew III	Salvage/Bury
Tanks	Crew III	Tails

LEACH TRANSFER TANKS

Electrical	Electrician	----
Pumps	Crew III	Bury
Surge Vessel	Crew III	"

(END OF PHASE TWO)

PHASE THREE

REAGENT DOCK

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Electrical	Electrician	----
Piping	Crew IV	Bury
Steel Structure	Crew IV	Salvage/Bury

THREE U. S. FILTERS

Electrical	Electrician	----
Pumps	Crew IV	Salvage/Bury
Sump Pump	Crew IV	Lay Down Area
Piping	Crew IV	Bury
Filters	Crew IV	"

REAGENT TANKS

Electrical	Electrician	----
Pumps	Crew IV	Salvage/Bury
Piping	Crew IV	Bury
Tanks	Crew IV	Lay Down Area

ELECTRIC SHOP

Electrical	Electrician	----
Building	Crew I	Upper Quonset

AIR COMPRESSORS

Electrical	Electrician	----
Piping	Crew I	Bury
Air Compressors	Crew I	Upper Quonset
Receiver Tank	Crew I	Lay Down Area

SHIFT OFFICE

Siding	Crew II	Bury
--------	---------	------

CENTRIFUGE ROOM

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Electrical	Electrician	----
Centrifuge	Crew II	Lay Down Area
Piping	Crew II	Bury
Scrubber	Crew II	"
Building	Contractor	"
Structure	Contractor	Salvage/Bury

PORTABLE OFFICE (UPSTAIRS)

Electrical	Electrician	----
Building	Crew III	Store - Upper Quonset
Concrete	Crew III	Bury

UPSTAIRS OFFICES

Electrical	Electrician	----
Building	Crew III	Bury

DRYER'A' DRYER ROOM

Electrical	Electrician	----
Roof	Contractor	Bury
Siding (Inside)	Contractor	Bury
Scrubber	Crew IV	Lay Down Area
Duct Work	Crew IV	Bury
ID Fan	Crew IV	Lay Down Area
Cake Crusher	Crew IV	" " "
Dryer Drive	Crew IV	" " "
Piping	Crew IV	Bury
Control Panel	Electrician	Lay Down Area

(Dryer may be purchased as is where is)

DRYER'B' PACKAGING ROOM

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Electrical	Electrician	---
Siding	Crew I	Bury
Conveyor	Crew I	Lay Down Area
Console	Crew I	" " "
Sump Pump	Crew I	Salvage/Bury
Hopper	Crew I	Lay Down Area
Belt Conveyor	Crew I	" " "
Scale	Crew I	" " "

ROD MILL

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Electrical	Electrician	----
Liners	Crew II	Salvage/Bury
Piping	Crew II	Bury
Pumps	Crew II	Lay Down Area
Control Panels	Crew II	" " "
Overhead Crane	Crew II	Salvage
"I" Beam for Crane	Crew II	Salvage/Bury
Feed Chute	Crew II	Bury
Walkway (Rod Mill to Leach)	Contractor	Salvage/Bury
Walkway (Rod Mill to #4 Belt)	Contractor	Salvage/Bury
Rod Charger	Crew II	Lay Down Area
Heat Exchangers	Crew II	Salvage/Bury
Piping	Crew II	" "
Platform & Stairs	Contractor	" "
Steel Structure	Contractor	" "
Rod Mill	Contractor	Lay Down Area
Concrete Supports	Contractor	Bury

MCC BY ROD MILL

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Panels	Electrician	Lay Down Area
Cinder Block/Concrete	Contractor	Bury

<u>Item</u>	<u>CABLE TRAY</u> <u>Responsibility</u>	<u>Disposal</u>
Cable Tray	Electrician	Bury
 <u>LEACH TANKS</u>		
	<u>'A'</u>	
Electrical	Electrician	---
Agitators	Crew III	Bury
Drive Units	Crew III	Salvage/Bury
Tank Tops	Crew III	Bury
Piping	Crew III	"
Thickener Feed Pumps	Crew III	Salvage/Bury
 <u>'B'</u>		
#2-#1-#3 Tanks	Contractor	Bury
#9-#11-#13 Tanks	Contractor	"
#8-#10-#12 Tanks	Contractor	"
#4-#5-#6-#7 Tanks	Contractor	"
Concrete Curbing	Crew IV	"
Sump Pump	Crew IV	Salvage/Bury
Operator Station	Crew IV	Store-Upper Quonset
Steel Structures & Walkways	Contracor	Salvage/Bury
 <u>THREE PRECIPITATION SURGE TANKS</u>		
Electrical	Electrician	---
Pumps	Crew I	Salvage/Bury
Tank Tops	Crew I	Bury
Piping	Crew I	"
Tanks	Contractor	"

(END OF PHASE THREE)

WCG/5.23.85/ow

PHASE IV

MAIN MILL BUILDING

'A'

REMAINDER OF PIPING

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Piping	Crew III	Bury

'B'

FIRST AID ROOM

Electrical	Electrician	----
Siding	Crew IV	Bury
Structure	Contractor	Salvage/Bury

'C'

REST ROOM

Electrical	Electrician	----
Siding	Crew IV	Bury
Structure	Contractor	Salvage/Bury

'D'

REMAINDER OF SECOND LEVEL CONCRETE

Concrete	Crew I	Bury
----------	--------	------

'E'

BUILDING

Electrical	Electrician	----
Roof	Contractor	Bury
Siding	Contractor/Crew II	Bury
Structural Steel	Contractor/Crew III	Salvage/Bury

MILL WAREHOUSE

Electrical	Electrician	----
Roof	Contractor	Bury
Siding	Contractor/Crew IV	Bury
Structral Steel	Contractor	Salvage/Bury
Piping	Contractor	Bury

MILL MAINTENANCE SHOP

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Electrical	Electrician	----
Crane Steel	Contractor	Salvage/Bury
Shop Office	Crew I	Store - Upper Quonset
Roof	Contractor	Bury
Siding	Contractor/Crew I	Bury
Structural Steel	Contractor/Crew I	Salvage/Bury

CENTRAL HEAT PLANT

Electrical	Electrician	----
Roof	Contractor	Bury
Siding	Contractor	Bury
Structural Steel	Contractor	Salvage/Bury

REAGENT WAREHOUSE

Electrical	Electrician	----
Piping	Crew II	Bury
Roof	Contractor	Bury
Siding	Contractor/Crew II	Bury
Structural Steel	Contractor/Crew II	Salvage/Bury

CONCRETE

Break Up Remaining	Contractor	In Place
--------------------	------------	----------

WCG/5.28.85/ow

(End Of Phase IV)

PHASE V

ACCOUNTING BUILDING

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Electrical	Electrician	----
Remove Contents	Crew II	Salvage/Bury
Building	Contractor	Salvage/Bury
Concrete	Contractor	Break Up In Place

(Building May Be Sold)

MAIN OFFICE BUILDING

Electrical	Electrician	----
Remove Contents	Crew II	Salvage/Bury
Building	Contractor	Salvage/Bury
Concrete	Contractor	Break Up In Place

GARAGE & RECORD STORAGE BUILDING

Electrical	Electrician	----
Remove Contents	Crew II	Salvage/Bury
Building	Contractor	Salvage/Bury
Concrete	Contractor	Break Up In Place

HEAVY EQUIPMENT STORAGE BUILDING

Electrical	Electrician	----
Remove Contents	Crew III	Salvage/Bury
Building	Contractor	Salvage/Bury
Concrete	Contractor	Break Up In Place

200,000 GALLON WATER TOWER

Electrical	Electrician	----
Dismantle Tower	Contractor	Salvage/Bury
Concrete	Contractor	Break Up In Place

DEEP WELL PUMPHOUSE

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Electrical	Electrician	----
Pumps	Crew IV	Salvage
Building	Crew IV	Salvage/Bury
Concrete	Crew IV	Break Up In Place

GAS STATION & TANKS

Electrical	Electrician	----
Pumps	Electrician	Lay Down Area
Tanks	Crew I	" " "
Building	Crew I	Salvage/Bury
Concrete	Crew I	Break Up In Place

FIRE HYDRANT SYSTEM

Hoses	Crew II	Salvage/Bury
Hose Houses	Crew II	Bury
Hydrants	Crew II	Salvage/Bury
Concrete	Crew II	Break Up In Place

FIRE WATER BOOSTER PUMPHOUSE

Electrical	Electrician	----
Diesel Tank	Crew III	Lay Down Area
Diesel Pump	Crew III	" " "
Electrical Pumps	Crew III	" " "
Piping/Valves	Crew III	Bury
Water Storage Tank	Contractor	Lay Down Area
Building	Contractor	Salvage/Bury
Structural Steel	Contractor	" "
Concrete	Contractor	Break Up In Place

YELLOWCAKE WAREHOUSE

<u>Item</u>	<u>Responsibility</u>	<u>Disposal</u>
Electrical	Electrician	----
Roof	Contractor	Salvage/Bury
Siding	Contractor	" "
Structural Steel	Contractor	" "
Concrete	Contractor	Break Up In Place

UPPER QUONSET WAREHOUSE

Electrical	Electrician	----
Contents	Crew IV	Salvage/Bury
Concrete	Contractor	Break Up In Place
Building	Contractor	Salvage/Bury
Side Building	Crew IV	Bury

REMAINING ITEMS

Fencing	Crew I	Salvage/Bury
Poles	Crew II	" "
Sidewalks	Crew III	Break Up In Place
Paving	Crew IV	Rip Up In Place

(End Of Phase V)

WCG/5.28.85/ow
