


Vogtle Unit 4 3Q/2021 Performance Summary

[Construction Action Matrix Column:](#)
[Licensee Response](#)

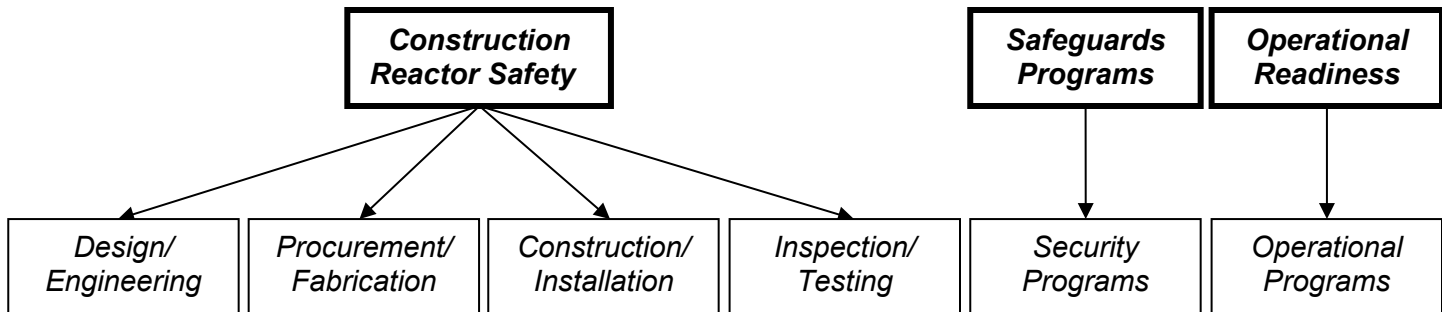

Most Significant Inspection Findings

3Q/2021	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter
2Q/2021	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter
1Q/2021	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter
4Q/2020	No findings this quarter	No findings this quarter	No findings this quarter	G	No findings this quarter	No findings this quarter

Additional Inspection and Assessment Information

- ❖ [List of Construction Inspection Reports](#)
- ❖ [List of Construction Assessment Reports/Inspection Plans](#)
- ❖ [Vogtle Unit 4 Findings Archive](#)

Design Engineering

[Back to Top](#)

Procurement/Fabrication

[Back to Top](#)

Construction/Installation

[Back to Top](#)

Inspection/Testing

Identified By: NRC

Identification Date: 11/04/2020

Significance: Green

Item Type: ITAAC Finding

Report: Vogtle Electric Generating Plant, Units 3 And 4 - NRC Integrated Inspection Reports

05200025/2020004, 05200026/2020004

Item Number: 05200026/2020002-02

Note: Closed in Report (NCV)

Failure to Construct and Perform Quality Inspections on the Battery Racks for the Class 1E DC and Uninterruptible Power Supply System

The inspectors identified an ITAAC finding of very low safety significance with an associated NCV of 10 CFR 50, Appendix B, Criterion V, "Instructions, Procedures, and Drawings." The licensee failed to construct and perform quality inspections on Unit 3 and Unit 4 Class 1E DC and uninterruptible power supply system (IDS) battery racks for the 250 Vdc 24-hour, 72-hour, and spare batteries in accordance with ITAAC 2.6.03.02.i and the approved design requirements for Vogtle Units 3 and 4. The licensee entered this finding into its CAP as CR 50066999, conducted engineering analysis of the nonconforming conditions, and performed rework on the battery racks to correct the nonconforming conditions.

This performance deficiency was of more than minor safety significance, and thus a finding, because it was material to the acceptance criteria of an ITAAC and invalidated the Inspection, Test, or Analyses described in the ITAAC 2.6.03.02.i. This finding was not associated with a security program; it was not associated with an IMC 2504 operational or construction program; and it was not associated with a repetitive, NRC-identified omission of a program critical attribute. This finding was a licensee performance deficiency of very low safety significance because it was associated with the IDS and there was reasonable assurance the design function of the system would not have been impaired by the deficiency based on engineering analysis of the nonconforming conditions identified. The inspectors determined this finding was indicative of present licensee performance and affected the cross-cutting area of human performance and the cross-cutting aspect of avoiding complacency. The proximate cause of the performance deficiency was primarily attributed to a failure to perform a thorough review of the work instructions and to plan the activity every time without relying on past successes and assumed conditions. [H.12] (Section 1A15)

[Back to Top](#)

Security Programs

[Back to Top](#)

Operational Programs

[Back to Top](#)
