

J. A. JONES CONSTRUCTION COMPANY
SPECIAL PROCESS PROCEDURE

FOR
ADDITIONAL GROUTING

OF
499S02-10B

WATERFORD SES UNIT NO. 3
CONTRACT NO. W3-NY-4

REV.	DATE	ENGINEERING REVIEWED BY	DATE	CONSTRUCTION REVIEWED BY	DATE	QUALITY ASSURANCE APPROVED BY	DATE
0	3-21-77	<i>C. Long</i>	3-22-77	<i>P. E. Harris</i>	3-22-77	<i>Robert William</i>	3-22-77
1	4-19-77	<i>A. H. H.</i>	4-19-77	<i>P. E. Harris</i>	4-19-77	<i>Robert William</i>	4-20-77

B506220120 B50222
PDR FOIA PDR
GARDEB4-455

FREEDOM OF INFORMATION
ACT REQUEST

84-455

C/632



SPECIAL PROCESS PROCEDURE	PROCEDURE NO. W-SP-17
TITLE OF PROCEDURE: ADDITIONAL GROUTING OF PLACEMENT 499S02-108	Issue Date: 3-21-77
PROJECT TITLE: WATERFORD SES UNIT #3	Rev. No. & Date: 1 4-19-77

1.0 PURPOSE

The purpose of this procedure is to outline the methods to be used by J. A. Jones Construction Company and Subcontractors to perform additional grouting of placement 499S02-108 as directed by letter #F-15396, dated 4-15-76 and letter #F-15449, dated 4-18-76, from Ebasco Services, Incorporated.

2.0 SCOPE

This procedure includes the requirements for further grouting of placement 499S02-108.

3.0 REFERENCES

3.1 Ebasco Services, Incorporated Letters F-15396 and F-15449.

3.2 ACI-503, Guide for use of Epoxy compounds with concrete.

3.3 Adhesive Engineering Company Technical Bulletin Numbers AE-354/1, AE-408/1, and Specification Number AEMS 309.

3.4 J. A. Jones Special Process Procedure, W-SP-13, Revision 3.

3.5 J. A. Jones Special Process Procedure, W-WP-7, Revision 6.

4.0 DEFINITIONS

4.1 Engineer: Ebasco Services, Incorporated.

4.2 Grout Refusal: A pressure of 180 PSI \pm 15 PSI that has stabilized for a period of approximately five (5) minutes.

5.0 RESPONSIBILITY

5.1 Ebasco Services, Incorporated shall be responsible for documentation review, acceptance, and determining if further grouting is necessary.

5.2 J. A. Jones Construction Company and Subcontractors shall be responsible for the coring, purchasing, receiving and acceptance of grouting materials, grouting operation, quality verification inspection, and documenting information for review by the Engineer.

5.3 J. A. Jones Construction Company shall have a qualified supervisor present during all grouting operations who shall be in responsible charge of the work.



SPECIAL PROCESS PROCEDURE	PROCEDURE NO. W-SP-17
TITLE OF PROCEDURE: ADDITIONAL GROUTING OF PLACEMENT 499S02-10B	Issue Date: 3-21-77
PROJECT TITLE: WATERFORD SES UNIT #3	Rev. No. & Date: 1 4-19-77

6.0 MATERIAL QUALIFICATION

- 6.1 The grouting material, Concessive 1380*, shall meet the requirements of Reference 3.4, J. A. Jones Special Process Procedure W-SP-13, Revision 3, Paragraphs 6.6 and 6.7.

7.0 CORING OF GROUT HOLES

- 7.1 At the locations specified in paragraph 7.2, the surface shall be chipped to expose the top mat of reinforcing steel.
- 7.2 Nine (9) two (2) inch diameter cores shall be drilled to a depth of seven (7) foot at the locations specified by numbers 1A through 9A on Attachment 1.
- 7.3 Core logs shall be initiated for each core containing the core and piece number, depth and questionable areas. All holes shall be plugged after drilling.
- 7.4 After cores are drilled they shall be labeled, stored in core boxes, and photographed.
- 7.5 Additional cores shall be drilled at the direction of the Engineer in accordance with paragraph 7.1 through 7.4.

8.0 GROUTING

- 8.1 The measurement of grout shall be accomplished with a dip stick (standard ruler) attached to the "B" component reservoir. Measurements shall be taken before and after injection into each grout hole and recorded in the remarks section of Attachment C. If the reservoir requires filling during the grouting of any hole, measurements shall be taken before and after filling the "B" reservoir and recorded. The quantity of grout used shall equal three (3) times the calculated volume of "B" component.
- 8.2 The volume of each grout hole shall be calculated from measurements taken of each grout hole before injection. The estimate of grout for filling each hole shall be determined later by utilizing the void ratio of the aggregate as determined from the sieve analysis and the calculated volume of each grout hole.
- 8.3 The material and equipment checklist, Attachment B, shall be completed by Quality Verification Personnel before proceeding.
- 8.4 Complete Part "A" of the Inspection Checklist, Appendix C for each injection hole before grouting begins.



SPECIAL PROCESS PROCEDURE	PROCEDURE NO. W-SP-17
TITLE OF PROCEDURE: ADDITIONAL GROUTING OF PLACEMENT 499S02-108	Issue Date: 3-21-77
PROJECT TITLE: WATERFORD SES UNIT #3	Rev. No. & Date: 1 4-19-77

8.5 Begin grouting lines A-A and C-C from East to West. Beginning with holes 1A and 3A, checking to see if grout flows to the holes in row B-B or the five (5) four (4) inch diameter holes, 1B thru 5B.

8.6 Each hole shall be grouted to refusal or until grout is observed in another location.

8.7 Drill eight (8) additional 2" diameter holes in lines D-D and E-E to a depth of seven (7) feet. Drilling and documentation shall be in accordance with section 7.

8.8 Grout lines D-D and E-E as outlined in paragraphs 8.1 thru 8.6 above.

8.9 Upon completion of 8.8 above a determination of which of the following paragraphs best describes the condition encountered will be made. Proceed accordingly as described below.

8.9a All holes do not take an excess of grout. Grout the holes in Row B-B and 1B thru 5B as outlined in 8.1 thru 8.6 above. Verification cores shall be taken at the direction of the Engineer.

8.9b One or more of the holes is questionable and no grout appears in row B-B or holes 1B thru 5B. Holes shall then be drilled as indicated by triangles on Attachment D in accordance with section 7. Grout these holes as outlined in paragraphs 8.1 thru 8.6 above.


8.9c One or more of the holes is questionable and appears in Row B-B or in holes 1B thru 5B. Holes shall then be drilled as indicated by triangles on Attachment E in accordance with section 7. Grout these holes as outlined in paragraphs 8.1 thru 8.6 above.

9.0 INSPECTION

9.1 J. A. Jones Quality Verification shall complete the applicable appendixes during the grouting operations.

9.2 Quality Verification personnel during the grouting operations shall inspect surrounding cores for influence of grout.

9.3 Any direction recieved from the Engineer during the completion of the repair shall be in written form, signed and dated, and included in Q.V. Documentation.



SPECIAL PROCESS PROCEDURE	PROCEDURE NO. W-SP-17
TITLE OF PROCEDURE: ADDITIONAL GROUTING OF PLACEMENT 499S02-10B	Issue Date: 3-21-77
PROJECT TITLE: WATERFORD SES UNIT #3	Rev. No. & Date: 1 4-19-77

10.0 ACCEPTANCE


10.1 After completion of the grouting operation, documentation shall be transmitted to the Engineer for review and discussion.

11.0 ATTACHMENTS

- A. Core Grid Locations
- B. Material and Equipment Checklist
- C. Inspection Checklist
- D. Excess Grout Take Grid
- E. Observed Grout Take Grid
- F. Previous Coring and Grouting Locations.

N4213.50

North

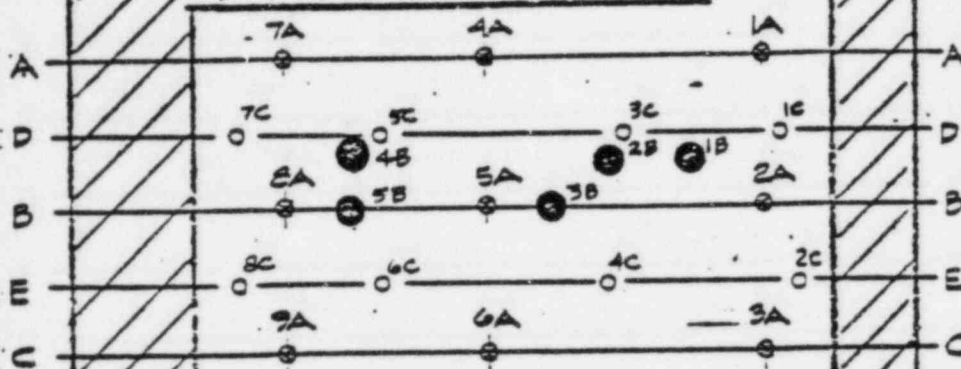

43922.50

24145.00

N4145.00

BLOCK 10B

- — NEW CORE HOLES (2" ϕ)
 ⊗ — PREVIOUSLY DRILLED HOLES (2" ϕ)
 ● — PREVIOUSLY DRILLED HOLES (4" ϕ)

ATTACHMENT A

MATERIAL AND EQUIPMENT CHECKLIST

MATERIALS

ACCEPT

REJECT

250 lbs. washed and dried bagged aggregate
50 gals. of Concessive* 1380 epoxy grouting material
1/4" tubing with Certification
12 1/4" screw plugs
25 lbs. plug setting material
1/4" packing gland fittings for 1/4" tube
12 tubing connectors 1/4" tubing to quick connect
quick disconnects
Waterless hand cleaner

_____	_____
_____	_____
_____	_____
_____	_____
_____	_____
_____	_____
_____	_____
_____	_____

EQUIPMENT

Packers with vents and entry port for 2" and 4" diameter
grout holes
4 grouting machines with mixing heads
6 flashlights with bulbs and batteries
vacuum cleaner
power outlets connected to one source with equal
back up system connected to independent source with tag
to "DO NOT DISCONNECT WITHOUT NOTIFYING J. A. JONES
SUPERVISOR LOCATED ON PLACEMENT 10B
Air source
0 to 200 PSI minimum pressure gauges with Certification
2 portable light stands with lights
Barrier rope with AUTHORIZED PERSONNEL ONLY signs
Protective glasses for all personnel
1 gang box with lock
Tubing cutter

_____	_____
_____	_____
_____	_____
_____	_____
_____	_____
_____	_____
_____	_____
_____	_____
_____	_____
_____	_____
_____	_____

INSPECTED BY: _____

TIME/DATE: _____

INSPECTION CHECKLIST

1. Material and Equipment Checklist
2. Area Chipped and Cleaned
3. Hole Clean
4. Grout Tube Installed
5. Grout Hole Filled with Aggregate
6. Packer Installed
7. Fitting Installed

ACCEPT

REJECT

INSPECTOR: _____

SHIFT: _____

DATE: _____

RT B

Estimated Time of Pumping _____

Estimated Quantity of Epoxy Injected _____


Remarks: _____

INSPECTOR: _____

SHIFT: _____

DATE: _____

N

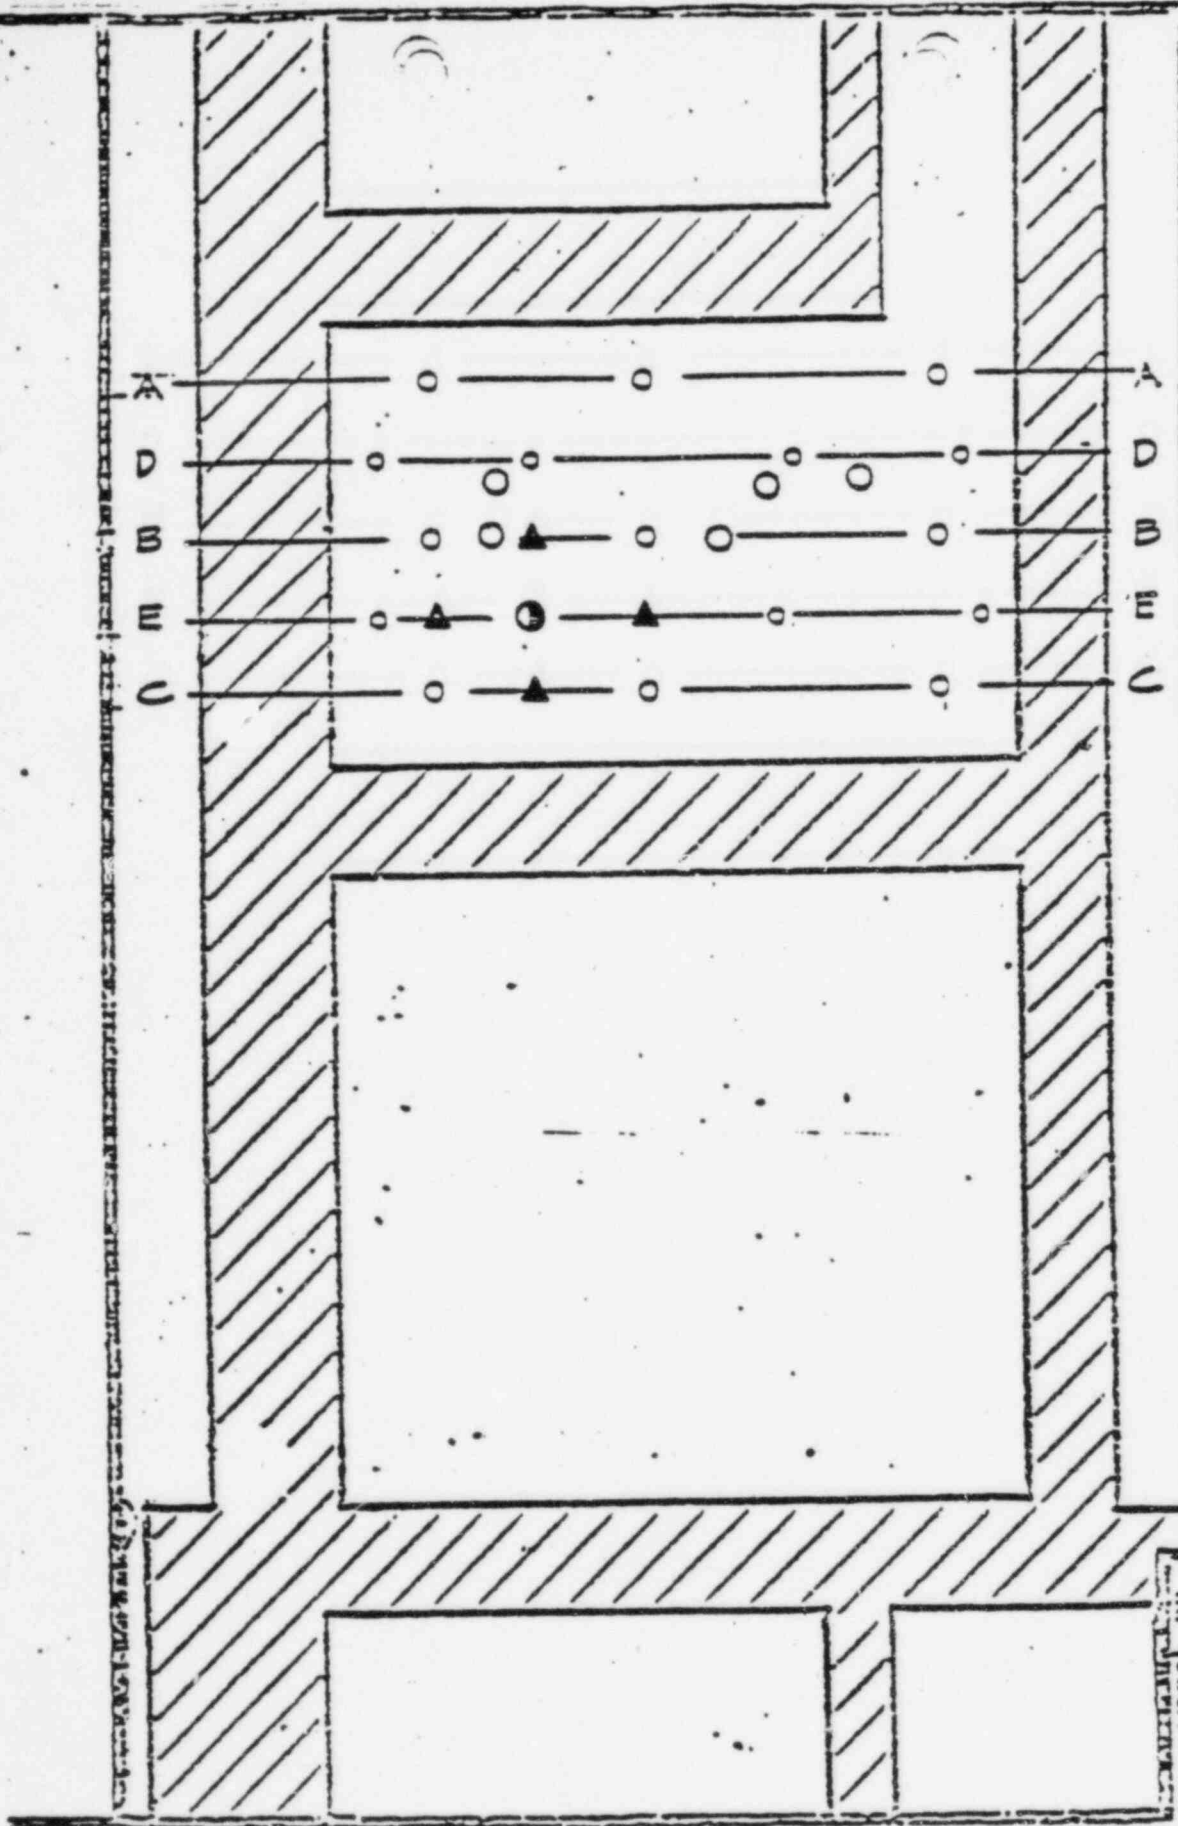

03922.50

03926.00


04145.00

BLOCK 10B

- — HOLE W/ EXCESS GROUT TAKE - CASE 2
- ▲ — NEW 2" ϕ GROUT HOLES

ATTACHMENT C

N4213.50

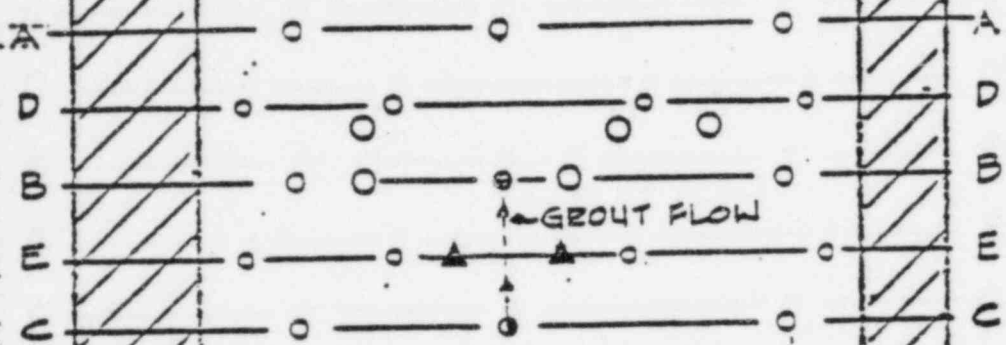

W3922.50

W3926.00

N4145.00


BLOCK 10B

- — HOLE W/ EXCESS GROUT TAKE - CASE 3
- ▲ — NEW 2" GROUT HOLES
- ⊕ — GROUT FLOW OBSERVED

ATTACHMENT E

ILL HOLE AND HONEYCOMBED AREA

N4213.50



N4145.00

N4145.00

(SEE J.A. JONES CURVE LOGS
FOR EXACT LOCATIONS)

ATTACHMENT F
