

August 17, 2012

Dominion 6/7/2012

North Anna 3 COLA

Meeting Presentation:


US – APWR DCWG

Licensing Actions

This schedule graphic contains public information about the NRC review schedules for the three US-APWR DCWG licensing actions and Dominion's assumptions regarding those activities.

Note: Issuance of the R-COL and S-COL is staggered one and two months, respectively, after issuance of the DCD

## US-APWR DCWG Licensing Actions

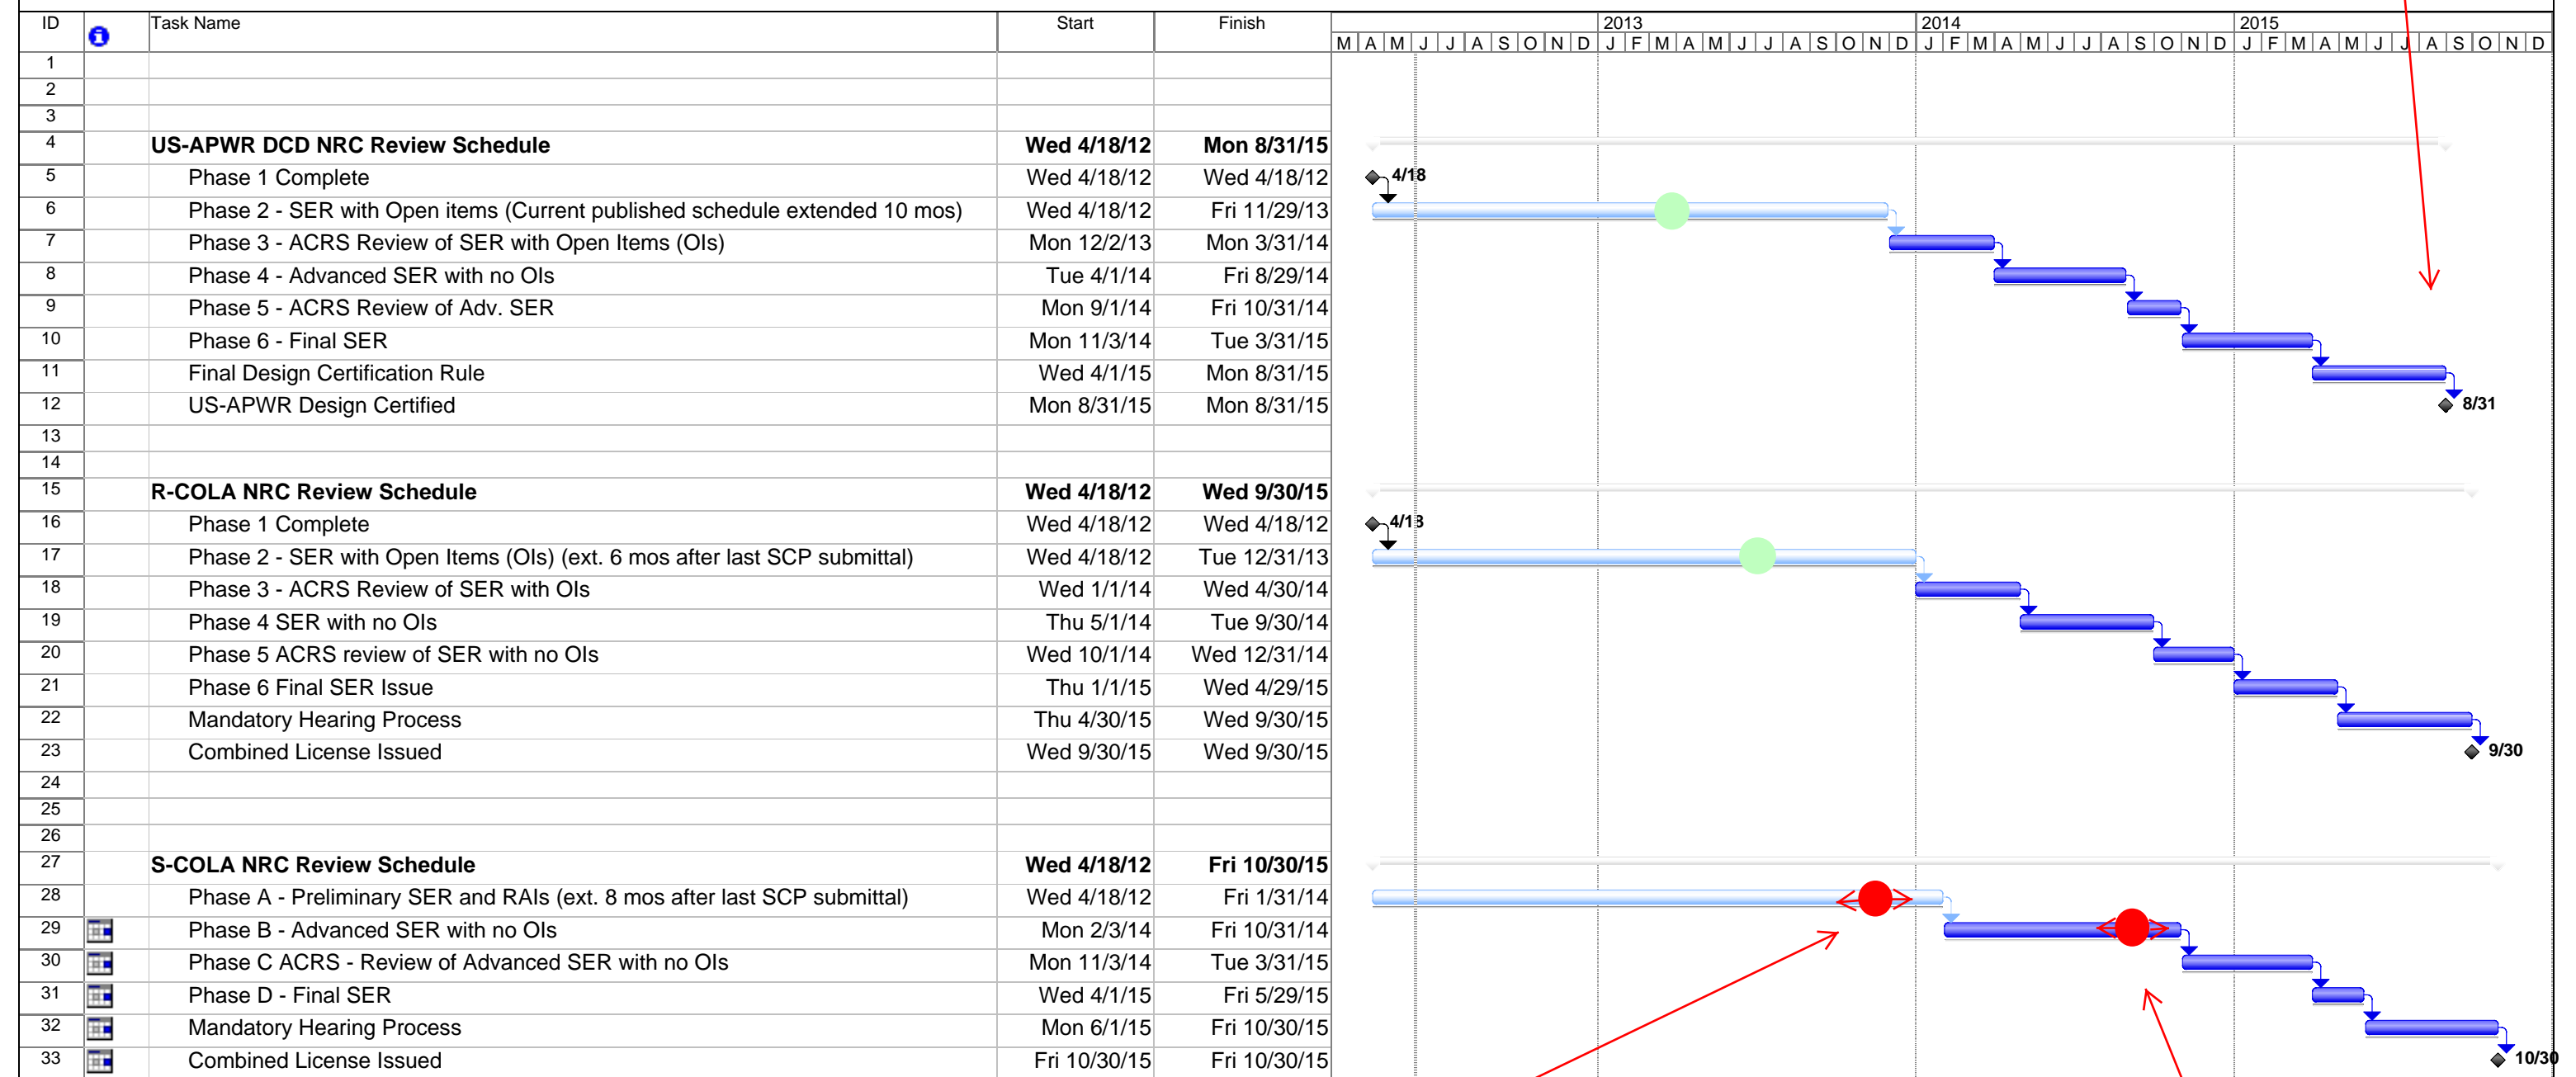

Project: 052212 USAPWR DCWG Lic  
Date: Tue 6/5/12

Task  
Split

## Progress



## Summary



## ~~External Tasks~~



Deadline



Split



### Milestone



## Project Summary



### External Milestones



Page 1

**Legend:**  
Red Ball - Indicates target timeframe for S-COLA revision  
Green Ball - Indicates planned DCD or R-COLA revision  
Light Blue Line - Current NRC review phase  
Dark Blue Line - Later NRC review phases. Phase durations consistent with latest published schedules.

A S-COLA revision targeted in late 2013 is proposed in order to:

- \* Maximize the opportunity to incorporate new or revised information driven by DCD Rev. 4 (planned for submittal in March 2013)
- \* Reflect the results of NRC's review of Dominion's various seismic closure plan (SCP) submittals scheduled from July 2012 to May 2013
- \* Incorporate the results of Dominion responses to NRC SCP-related RAIs

This COLA revision would serve as the basis for entry into Phase B

A S-COLA revision targeted in late Summer or early Fall 2014 is proposed in order to:

- \* Reflect the resolution of the open items dispositioned during the Phase B NRC review
- \* Provide adequate time for NRC to conduct confirmatory reviews of any outstanding items that NRC would expect to see in the S-COLA revision

This COLA revision would serve as the basis for entry into Phase C
