



52-001


GE Nuclear Energy11/13/92
ABWRDate 11/13/92To Chet PoslusnyFax No. —This page plus 3 page(s)From Jack FoxMail Code 782
175 Curtner Avenue
San Jose, CA 95125Phone (408) 925-4824FAX (408) 925-1193
or (408) 925-1687Subject Proposed ABWR Certification
Process and ScheduleMessage _____

17-134

9211180299 921113
PDR ADOCK 05200001
A PDR

D050

Remaining ABWR Certification Process

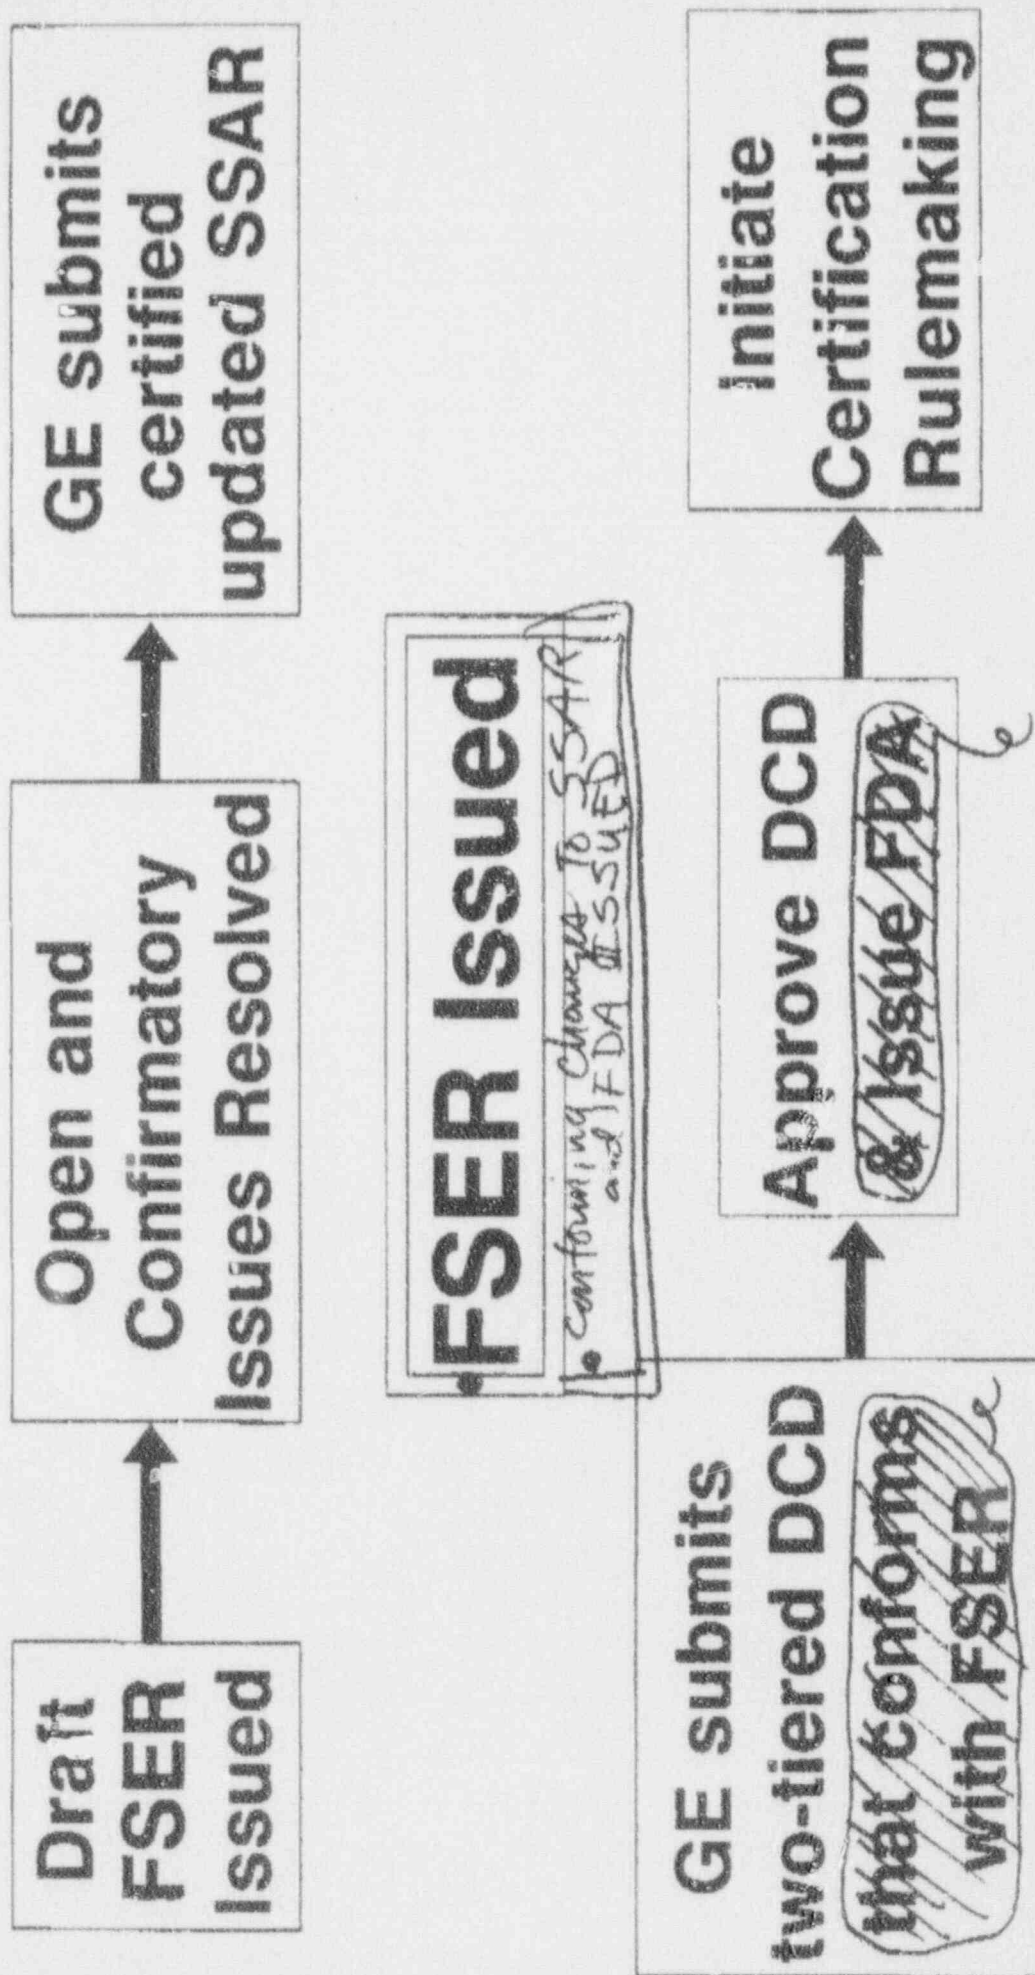

ABWR FDA SCHEDULE

Activity	Start Date	Finish Date	1992			1993						
			Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
DFSER Issued	11/1/92 10/20/92		▲									
Open/ Confirmatory Issues Resolution	10/1/92 10/1/92	3/1/93	■	■	■	■	■	■				
ACRS Review	9/30/92	2/28/93	■	■	■	■	■	■				
Final SSAR Preparation	1/15/93	4/1/93				■	■	■				
Final SSAR Issued	3/31/93							▲				
NRC SSAR Verification	4/1/93	5/1/93						■	■			
FSER Issued	4/30/93								▲			
Conforming Changes to SSAR	5/1/93	6/1/93							■	■		
FDA Issued	6/1/93									▲		
DCD Preparation/Submittal	4/1/93	5/18/93						■	■	■		
DCD Approval	5/18/93	6/30/93								■	■	
Initiate Certification	7/1/93										▲	

11/12/92

ABWR FDA SCHEDULE ASSUMPTIONS

~~TIER 1 BECOMES APPENDIX A OF THE SSAR~~

IC and Programmatic

- GENERALLY ITAAC ISSUE RESOLVED BY 12/92
- FINAL STAGE OF ACRS REVIEW DOES NOT RESULT IN ADDITIONAL STUDIES/DESIGN CHANGES
- NRC SSAR VERIFICATION DOES NOT RESULT IN SIGNIFICANT ADDITIONAL QUESTIONS OR SSAR CHANGES
