

6/28/2000

6/28/9

Final Report Concurrence Schedule for Spent Fuel Pool Accident Risk at Decommissioning Plants


ID	Task Name	Start	Finish	Jun 25, '00	Jul 02, '00	Jul 09, '00	Jul 16, '00	Jul 23, '00	Jul 30, '00
1	Tech. Branches address public & ACRS comments	Fri 04/07/00	Fri 07/07/00						
2	Projects Draft Cover Letter	Fri 07/07/00	Fri 07/21/00						
3	SPSB receive T/H technical input	Tue 06/27/00	Tue 06/27/00	◆ 06/27					
4	SPLB Receive PRA Input/Revisions	Fri 07/21/00	Fri 07/21/00					◆ 07/21	
5	SPLB Receive Seismic Input/Revisions	Fri 07/21/00	Fri 07/21/00					◆ 07/21	
6	SPLB Receive Thermal Hydraulic Input/Revisions	Fri 07/21/00	Fri 07/21/00					◆ 07/21	
7	SPLB Receive RES Input/Revision	Fri 07/21/00	Fri 07/21/00					◆ 07/21	
8	SPLB Receive tech. responses to other public comments	Fri 07/21/00	Fri 07/21/00					◆ 07/21	
9	All Technical Inputs/Revisions to SPLB	Mon 07/17/00	Fri 07/21/00						
10	SPLB prepares Final report	Mon 07/24/00	Wed 07/26/00						
11	pkg to BCs, Projects, DE, RES, tech. edit	Thu 07/27/00	Thu 07/27/00						
12	incorporate BC, DE, RES, Proj., tech.edit comments	Mon 07/31/00	Wed 08/02/00						
13	BC/DE concurrence	Thu 08/03/00	Thu 08/03/00						
14	other office concurrences & RES	Thu 08/03/00	Thu 08/03/00						
15	pkg to GMH, John Z. & B. Sheron	Fri 08/04/00	Fri 08/04/00						
16	Gary sign out package & Projects	Wed 08/09/00	Wed 08/09/00						
17	pkg to Brian	Tue 08/15/00	Tue 08/15/00						
18	Brian concur COB	Thu 08/17/00	Thu 08/17/00						
19	Package to Sam Collins & Roy Zimm.	Fri 08/18/00	Fri 08/18/00						
20	Sam concur and forward to EDO COB	Tue 08/22/00	Tue 08/22/00						
21	EDO Submit Final to Commission	Wed 08/23/00	Wed 08/23/00						

Project: &[TWG Final Report]
Date: Mon 06/26/00 2:41 PM

Task		Summary		Rolled Up Progress	
Split		Rolled Up Task		External Tasks	
Progress		Rolled Up Split		Project Summary	
Milestone	◆	Rolled Up Milestone	◇		

**Final Report Concurrence Schedule for
Spent Fuel Pool Accident Risk at Decommissioning Plants**

ID	Task Name	Start	Finish	Aug 06, '00	Aug 13, '00	Aug 20, '00	Aug 27, '00	Sep 03, '00	Sep 10, '00
1	Tech. Branches address public & ACRS comments	Fri 04/07/00	Fri 07/07/00						
2	Projects Draft Cover Letter	Fri 07/07/00	Fri 07/21/00						
3	SPSB receive T/H technical input	Tue 06/27/00	Tue 06/27/00						
4	SPLB Receive PRA Input/Revisions	Fri 07/21/00	Fri 07/21/00						
5	SPLB Receive Seismic Input/Revisions	Fri 07/21/00	Fri 07/21/00						
6	SPLB Receive Thermal Hydraulic Input/Revisions	Fri 07/21/00	Fri 07/21/00						
7	SPLB Receive RES Input/Revision	Fri 07/21/00	Fri 07/21/00						
8	SPLB Receive tech. responses to other public comments	Fri 07/21/00	Fri 07/21/00						
9	All Technical Inputs/Revisions to SPLB	Mon 07/17/00	Fri 07/21/00						
10	SPLB prepares Final report	Mon 07/24/00	Wed 07/26/00						
11	pkg to BCs, Projects, DE, RES, tech. edit	Thu 07/27/00	Thu 07/27/00						
12	incorporate BC, DE, RES, Proj., tech.edit comments	Mon 07/31/00	Wed 08/02/00						
13	BC/DE concurrence	Thu 08/03/00	Thu 08/03/00	/03					
14	other office concurrences & RES	Thu 08/03/00	Thu 08/03/00	/03					
15	pkg to GMH, John Z. & B. Sheron	Fri 08/04/00	Fri 08/04/00						
16	Gary sign out package & Projects	Wed 08/09/00	Wed 08/09/00						
17	pkg to Brian	Tue 08/15/00	Tue 08/15/00						
18	Brian concur COB	Thu 08/17/00	Thu 08/17/00						
19	Package to Sam Collins & Roy Zimm.	Fri 08/18/00	Fri 08/18/00						
20	Sam concur and forward to EDO COB	Tue 08/22/00	Tue 08/22/00						
21	EDO Submit Final to Commission	Wed 08/23/00	Wed 08/23/00						

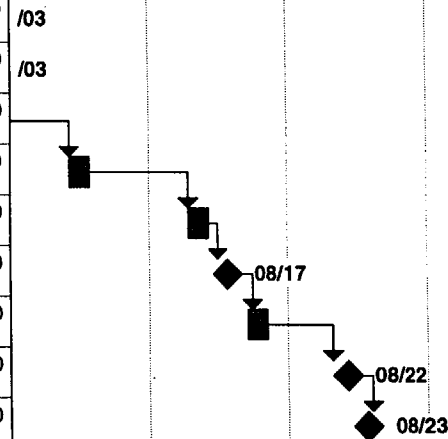

Project: &[TWG Final Report]
Date: Mon 06/26/00 2:41 PM

Task

Split

Progress

Milestone

Summary

Rolled Up Task

Rolled Up Split

Rolled Up Milestone

Rolled Up Progress

External Tasks

Project Summary
