

TRANSMITTAL OF MEETING HANDOUT MATERIALS FOR IMMEDIATE PLACEMENT IN THE PUBLIC DOMAIN

*This form is to be filled out (typed or hand-printed) by the person who announced the meeting (i.e., the person who issued the meeting notice). The completed form, and the attached copy of meeting handout materials, will be sent to the Document Control Desk on the same day of the meeting; under no circumstances will this be done later than the working day after the meeting.
Do not include proprietary materials.*

DATE OF MEETING

5/21/01

The attached document(s), which was/were handed out in this meeting, is/are to be placed in the public domain as soon as possible. The minutes of the meeting will be issued in the near future. Following are administrative details regarding this meeting:

Docket Number(s)

50-338, 50-339, 50-280, 50-281, 50-413,
50-414, 50-369, 50-370, 50-227
~~50-278~~

Plant/Facility Name

Surry, North Anna, McGuire,
Catawba, & Peach Bottom

TAC Number(s) (if available)

Reference Meeting Notice

5/8/01

Purpose of Meeting
(copy from meeting)

The NRC staff is developing an improved schedule model for the review of license renewal applications based on the experience gained from the first applications. The model will reflect the current process being used for reviewing renewal applications and will provide the flexibility needed to adjust interim milestones to accommodate the high level of work expected resulting from receipt of five applications in 2001 within approximately one month of each other. This meeting begins discussions with the three applicants planning 2001 renewal submittals to develop an integrated schedule using the new model.

NAME OF PERSON WHO ISSUED MEETING NOTICE

Stephen T. Hoffman

TITLE

Sr. Proj. Mgr.

OFFICE

NRR

DIVISION

DRIP

BRANCH

RLSB

Distribution of this form and attachments:

Docket File/Central File
PUBLIC

DF01

NRC STAFF LICENSE RENEWAL SCHEDULE MEETING
WITH VEPCO, DUKE, AND EXELON
MAY 21, 2001

Purpose

Discuss the revised license renewal schedule model and gather information for developing integrated review schedules for the renewal applications to be submitted in 2001.

Desired Outcome

VEPCO, Duke, and Exelon representatives understand the NRC staff's development of the new schedule model and have an opportunity to provide their views on the new model and plant-specific information (e.g., outage schedules) for the staff's use in developing plant-specific renewal application review schedules.

Agenda

- | | | |
|---|--|-------------------------|
| 1. Introduction | 1:30-1:35 pm | NRC
Grimes |
| 2. Revised license renewal schedule model | 1:35-1:50 pm | NRC
Koenick |
| 3. Draft application review schedules | | |
| a. Overview of schedules and integration
with ongoing activities | 1:50-2:10 pm | NRC
Koenick |
| b. Licensee assessment | 2:10-2:25 pm
2:25-2:40 pm
2:40-2:55 pm | VEPCO
Duke
Exelon |
| 4. Integration of the 3 reviews and
levelizing resource demands | 2:55-3:25 pm | All |
| 5. Future actions | 3:25-3:30 pm | NRC
Grimes |

Draft License Renewal Application Review Schedule

Milestones	Target Day
Receive License Renewal Application	0
Application is accessible	17
FRN published for receipt & acceptability review	30
Press Release describing FRN	31
FRN published for Intent/Env Scoping mtg	35
FRN published describing acc./rejection	60
FRN published for opportunity for hearing	60
Press Release describing FRN	61
Environmental Scoping Meeting	75
Deadline for Filing Hearing Requests and Petitions for Intervention	90
EIS Scoping Period Ends	95
Env. RAls Issued to Applicant	145
Safety Audit Complete	150
Env. RAls Responses Issued to NRC	205
Safety RAls issued by RLSB	240
Responses to Safety RAls received	315
Draft SEIS to EPA, Issue Notice of Availability	335
Scoping Inspection Complete	345
Public Meeting to Discuss DEIS	370
End of DEIS Comment Period	385
AMR Inspection Complete	405
SER w/OI issued by RLSB	435
ACRS Subcommittee of SER OI	465
ACRS Full committee of SER OI	480
Responses to SER OI received	510
Final SEIS issued to EPA/Issue Notice of Availability	540
Optional Final Inspection complete	550
SER issued by RLSB	585
Regional Administrator's Letter	600
ACRS Subcommittee of SER	615
ACRS of full committee of SER	630
SER issued as NUREG	630
ACRS Letter	645
Commission Paper W/Staff Recommendations	805
Commission Decision	900

May 9, 2001

DRAFT Dominion Joint LRA Review Schedule

Milestone	Target Date	Target Day
Receive License Renewal Application	5/29/01	0
Application is accessible	6/15/01	17
FRN published for receipt & acceptability review	6/28/01	30
Press Release describing FRN	6/29/01	31
FRN published for Intent/Env Scoping mtg	7/9/01	35
FRN published describing acc./rejection	7/30/01	60
FRN published for opportunity for hearing	7/30/01	60
Press Release describing FRN	7/31/01	61
Environmental Scoping Meetings	8/13/01	75
Deadline for Filing Hearing Requests and Petitions for Intervention	8/28/01	90
EIS Scoping Period Ends	9/5/01	95
Env. RAls Issued to Applicant	10/22/01	145
Safety Audits Complete	10/29/01	150
Env. RAls Responses Issued to NRC	12/19/01	205
Safety RAls issued by RLSB	1/28/02	240
Scoping Inspections Complete	2/15/02	345
Responses to Safety RAls received	4/15/02	315
Draft SEIS to EPA, Issue Notice of Availability	4/29/02	335
AMR Inspections Complete	5/31/02	405
Public Meeting to Discuss DEIS	6/7/02	370
End of DEIS Comment Period	6/17/02	385
SER w/OI issued by RLSB	8/12/02	435
ACRS Subcommittee of SER OI	9/9/02	465
ACRS Full committee of SER OI	9/23/02	480
Responses to SER OI received	10/28/02	510
Final SEIS issued to EPA/Issue Notice of Availability	11/18/02	540
Optional Final Inspection complete	12/4/02	550
SER issued by RLSB	1/9/03	585
Regional Administrator's Letter	1/22/03	600
ACRS Subcommittee of SER	2/6/03	615
ACRS of full committee of SER	2/20/03	630
SER issued as NUREG	2/25/03	630
ACRS Letter	3/6/03	645
Commission Paper W/Staff Recommendations	8/29/03	805
Commission Decision	12/4/03	900

May 16, 2001

DRAFT Duke Joint LRA Review Schedule

Milestone	Target Date	Target Day
Receive License Renewal Application	6/14/01	0
Application is accessible	7/3/01	17
FRN published for receipt & acceptability review	7/16/01	30
Press Release describing FRN	7/17/01	31
FRN published for Intent/Env Scoping mtg	7/25/01	35
FRN published describing acc./rejection	8/15/01	60
FRN published for opportunity for hearing	8/15/01	60
Press Release describing FRN	8/16/01	61
Environmental Scoping Meetings	8/29/01	75
Deadline for Filing Hearing Requests and Petitions for Intervention	9/13/01	90
EIS Scoping Period Ends	9/21/01	95
Env. RAls Issued to Applicant	11/7/01	145
Safety Audits Complete	11/14/01	150
Env. RAls Responses Issued to NRC	1/4/02	205
Safety RAls issued by RLSB	2/13/02	240
Scoping Inspections Complete	3/29/02	345
Responses to Safety RAls received	5/1/02	315
Draft SEIS to EPA, Issue Notice of Availability	5/15/02	335
Public Meeting to Discuss DEIS	6/25/02	370
End of DEIS Comment Period	7/3/02	385
AMR Inspections Complete	8/2/02	405
SER w/OI issued by RLSB	8/28/02	435
ACRS Subcommittee of SER OI	9/25/02	465
ACRS Full committee of SER OI	10/9/02	480
Responses to SER OI received	11/13/02	510
Final SEIS issued to EPA/Issue Notice of Availability	12/4/02	540
Optional Final Inspection complete	12/20/02	550
SER issued by RLSB	1/27/03	585
Regional Administrator's Letter	2/7/03	600
ACRS Subcommittee of SER	2/24/03	615
ACRS of full committee of SER	3/10/03	630
SER issued as NUREG	3/13/03	630
ACRS Letter	3/24/03	645
Commission Paper W/Staff Recommendations	9/16/03	805
Commission Decision	12/22/03	900


May 16, 2001

DRAFT Peach Bottom LRA Review Schedule

Milestone	Target Date	Target Day
Receive License Renewal Application	7/2/01	0
Application is accessible	7/19/01	17
FRN published for receipt & acceptability review	8/1/01	30
Press Release describing FRN	8/2/01	31
FRN published for Intent/Env Scoping mtg	8/10/01	35
FRN published describing acc./rejection	8/31/01	60
FRN published for opportunity for hearing	8/31/01	60
Press Release describing FRN	9/3/01	61
Environmental Scoping Meeting	9/14/01	75
Deadline for Filing Hearing Requests and Petitions for Intervention	10/1/01	90
EIS Scoping Period Ends	10/9/01	95
Env. RAls Issued to Applicant	11/23/01	145
Safety Audit Complete	11/30/01	150
Env. RAls Responses Issued to NRC	1/22/02	205
Safety RAls issued by RLSB	3/1/02	240
Responses to Safety RAls received	5/17/02	315
Draft SEIS to EPA, Issue Notice of Availability	5/31/02	335
Scoping Inspection Complete	6/14/02	345
Public Meeting to Discuss DEIS	7/11/02	370
End of DEIS Comment Period	7/19/02	385
AMR Inspection Complete	8/9/02	405
SER w/OI issued by RLSB	9/13/02	435
ACRS Subcommittee of SER OI	10/11/02	465
ACRS Full committee of SER OI	10/25/02	480
Responses to SER OI received	11/29/02	510
Final SEIS issued to EPA/Issue Notice of Availability	12/20/02	540
Optional Final Inspection complete	1/7/03	550
SER issued by RLSB	2/12/03	585
Regional Administrator's Letter	2/25/03	600
ACRS Subcommittee of SER	3/12/03	615
ACRS of full committee of SER	3/26/03	630
SER issued as NUREG	3/31/03	630
ACRS Letter	4/9/03	645
Commission Paper W/Staff Recommendations	10/2/03	805
Commission Decision	1/7/04	900

May 16, 2001

ESTIMATED Combined Resource Profile of FY 01 Applications

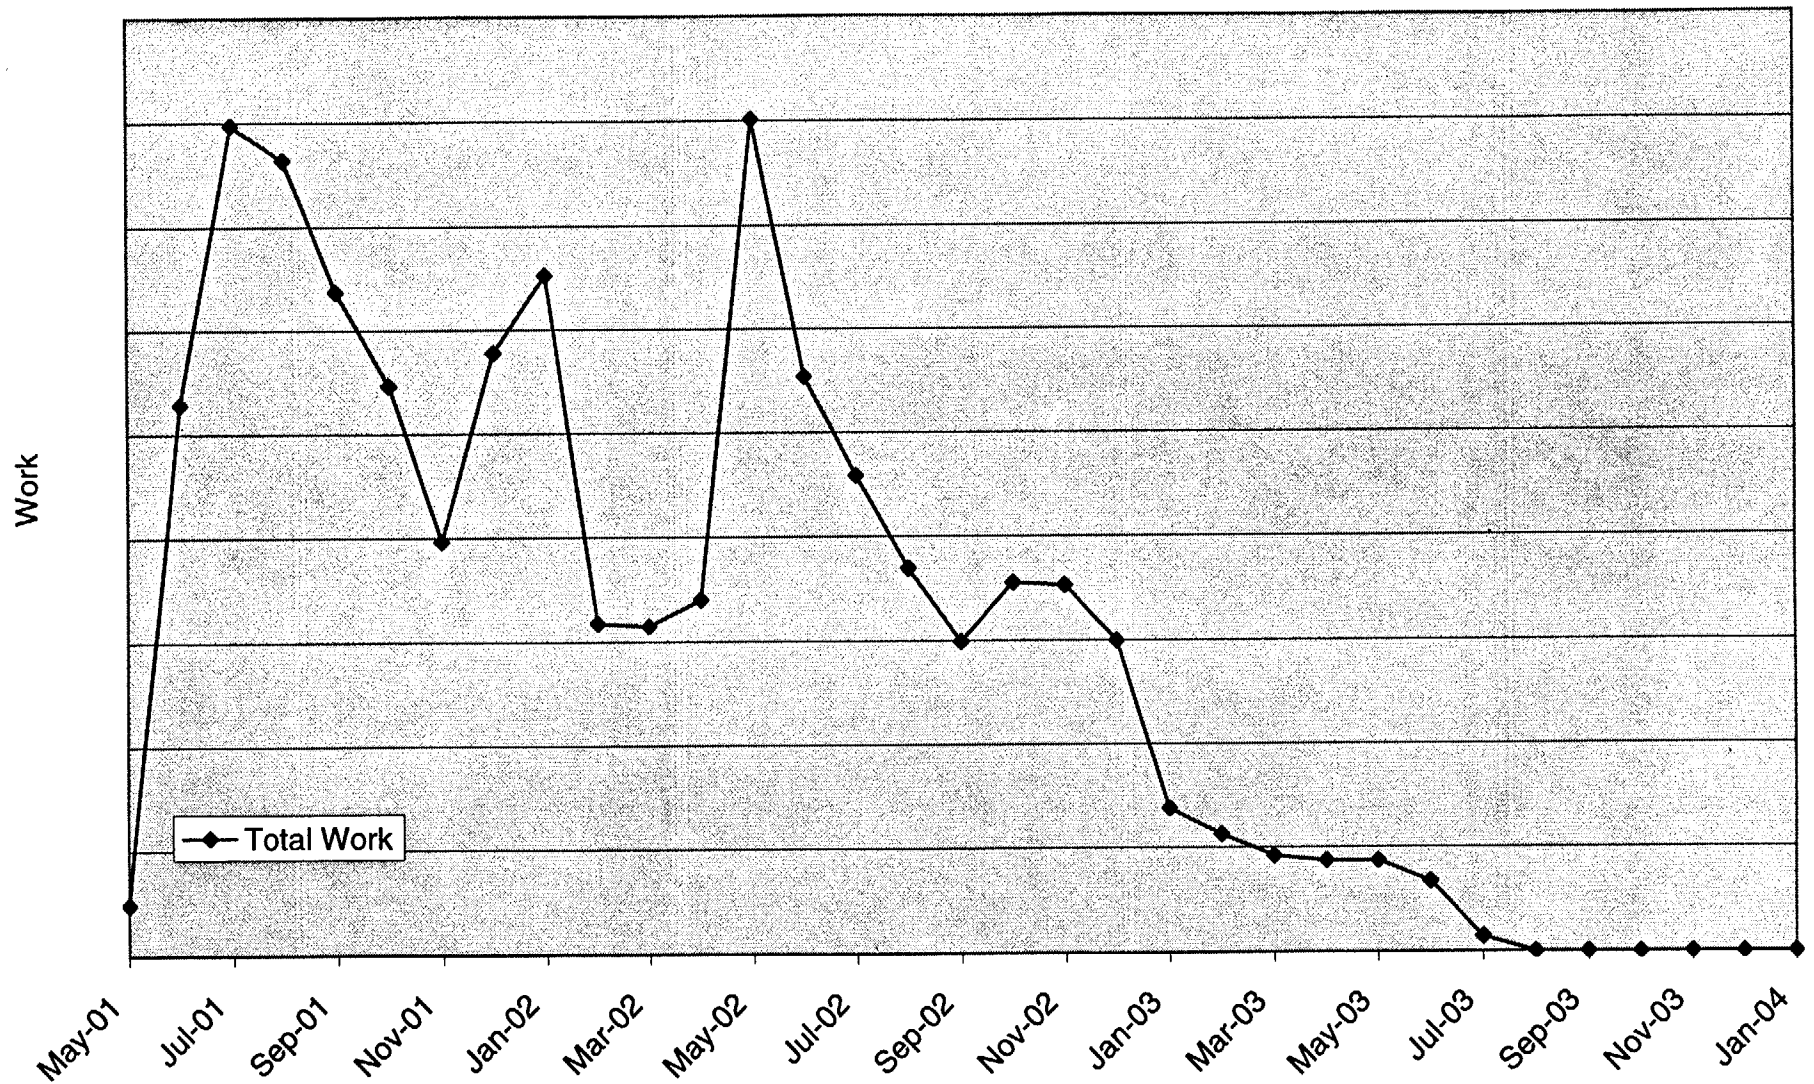

Applications: Dominion, Duke, Exelon.

Plants: Surry, North Anna, McGuire, Catawba, and Peach Bottom
